

SUPERVISOR MINUTES #7

Date:	27 December 2012
Time:	7:00 pm
Venue:	Skype
Attendees:	Can.One 1. Ardian Tjeng 2. Grace Shintany Lee 3. Melwin Tanu 4. Shira Aretti 5. Tai Shi Ling Supervisor Kyong Jin Shim
Absentees: (provide reason if any)	-
Agenda:	1. Updates on project management 2. Demo


DISCUSSION

No.	Details
-----	---------

1. **Updates on project management**

- Schedule metric score

Iteration	Planned Duration	Actual Duration	Schedule Metric Score
Iteration 1	18 days	19.33 days	0.93
Iteration 2	22 days	22.33 days	0.99
Iteration 3	8 days	9.67 days	0.83
Iteration 4	19 days	20 days	0.95
Iteration 5	19 days	21 days	0.90

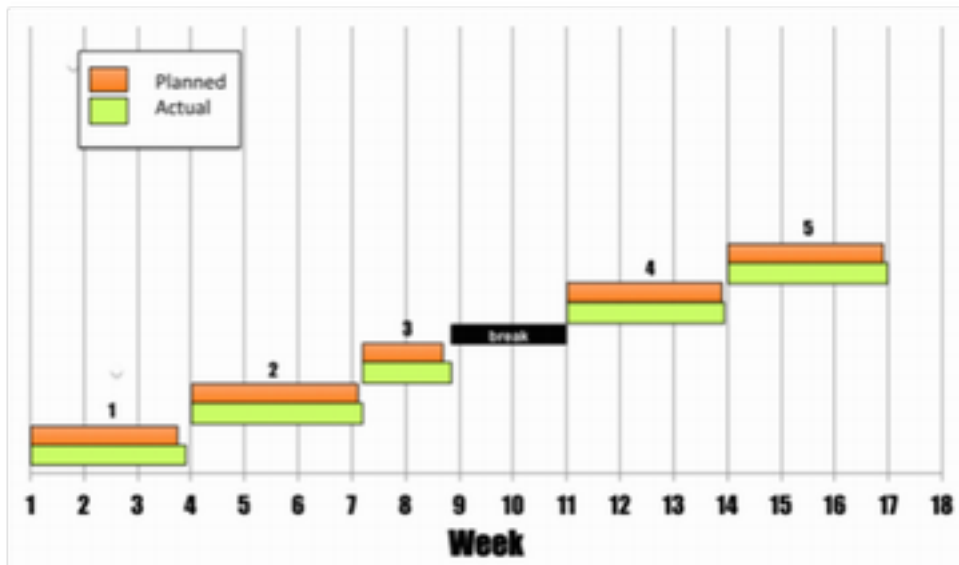

- [Test cases for iteration 5](#)
- [Bug tracking log](#)
- Iteration 6 - Task Allocation

Subject	Assigned to	Planned Duration (hour)
Iteration 6		
UI		
Integrate shopping cart (continue)	Ardian	6
Social UI	Ardian	15
Email and username taken validation	Melwin	1
Testing framework	Shi Ling	9
Registration process and validation	Shi Ling	9
Accessories - publish and unpublish	Shi Ling	3
Shopping		
Order status	Melwin	3
Past purchases	Melwin	6
Social		
Add, remove, view friends	Shira	12
Add, remove, view groups	Melwin	6
Chat	Melwin	3
Group chat	Melwin	3
Testing the Functionality for Iteration 6	Shira	3

Total hours per person:

- Ardian 21 hours
- Melwin 22 hours
- Shi Ling 21 hours
- Shira 15 hours

Availability schedule:

- Grace away from 28th Dec - 6th Jan (Jakarta)
- Melwin away from 29th Dec - 4th Jan (Hong Kong)
- Shi Ling away from 29th Dec - 2nd Jan (Malaysia)

2. **Updates from sponsor**

- Gamurai doesn't consolidate purchases from different vendor
- Gamurai will provide photos for VEON latest by 2nd Jan 2013
- Return policy: email

3.	<p>Demo</p> <ul style="list-style-type: none"> - Shi Ling: <ul style="list-style-type: none"> ● Testing Frame work ● Accessories - add/view/edit general and product design info - Shira: <ul style="list-style-type: none"> ● Change email & password - Ardian: <ul style="list-style-type: none"> ● UI integration for: <ul style="list-style-type: none"> ○ registration ○ shopping cart ○ payment
4.	<p>Supervisor's comment</p> <ul style="list-style-type: none"> - Testing frameworks <ul style="list-style-type: none"> ● What metrics can be used? <ul style="list-style-type: none"> ○ cyclomatic complexity - look through method and try to find different path; for each source file, it will give you report and bar chart to indicate how good is your code performing ● Finalized test cases for UI by January ● Deployment error <ul style="list-style-type: none"> ○ deploy image file into the file system and link it to relative path ○ should not deploy image all together at one time ○ do partial deployment (only deploy changes) ● Must login before check out ● Do what everyone else is doing <ul style="list-style-type: none"> ○ track order ○ billing information - save multiple & save for later ● Vendor portal - batch uploading must be done by midterm

TO-DOs

Task ID	Details	Date Due	Assigned To
1.	Testing metrics	TBA	Shi Ling
2.	Vendor portal - batch uploading	Midterm	Shi Ling
3.	Finalize UT test cases	11 Jan	Shira
4.	Solve deployment error	11 Jan	Melwin
5.	Order tracking and billing information	11 Jan	Melwin

NEXT SUPERVISOR MEETING

Date:	10 January 2013
Time:	7:00 PM
Venue:	TBA
Agenda:	Updates on progress

Meeting adjourned by: 8:15 PM

Minutes taken by: Tai Shi Ling

Vetted by: Grace Shintany Lee on 27 December 2012
