

ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names	% Complete		
								F	S
1		Note: 1 Day (Equivalent to 3 hours), 0 Days represent deadlines					0%		
2		<b>Inception Phase</b>	<b>49 days</b>	<b>Sat 12/5/12</b>	<b>Sat 30/6/12</b>	<b>All</b>	<b>0%</b>		
3		<b>Idea Generation Phase</b>	<b>28 days</b>	<b>Sat 12/5/12</b>	<b>Sat 9/6/12</b>		<b>0%</b>		
4		Idea Discussion Meetings	3 days			All	0%		
5		<b>Preliminary Idea Findings</b>	<b>14 days</b>	<b>Sat 12/5/12</b>	<b>Sat 26/5/12</b>		<b>0%</b>		
6		Get popularity Index feature and Internal Consulting Service	7 days	Sat 12/5/12	Sat 19/5/12	Larry	0%		
7		Worthy Cause Project- Match-Client	21 days	Sat 12/5/12	Sat 2/6/12	Jeffrey, Kevin	0%		
8		Reward System	21 days	Sat 12/5/12	Sat 2/6/12	Kevin	0%		
9		Share Worthy Cause project stories	21 days	Sat 12/5/12	Sat 2/6/12	Yi Zao	0%		
10		Feedback to Masami (Sponsor Meeting)	0 days	Sat 2/6/12	Sat 2/6/12	Zhang Yingyue	100%		
11		<b>Change and Reviewed Idea Findings- Android Application</b>	<b>7 days</b>	<b>Sun 3/6/12</b>	<b>Sun 10/6/12</b>	<b>All</b>	<b>0%</b>		
12		Discuss and confirm idea finding during sponsor meetings	0 days	Wed 6/6/12	Wed 6/6/12	All	0%		
13		Molecule Concept	5 days	Sun 3/6/12	Fri 8/6/12	Larry, Zheng Keli (TBC)	0%		
14		Media Management Concept	5 days	Sun 3/6/12	Fri 8/6/12	Jeffrey, Kevin (TBC)	0%		
15		Consolidate All Ideas	1 day	Fri 8/6/12	Sat 9/6/12	Zhang Yingyue	0%		
16		Final Review by project managers	1 day	Sat 9/6/12	Sun 10/6/12	Jeffrey, Kevin	0%		
17		Start meeting with supervisor and Professor Zhu	0 days	Sat 9/6/12	Sat 9/6/12	All	100%		
18		<b>Discussion of main plans for wiki page</b>	<b>0 days</b>	<b>Sat 9/6/12</b>	<b>Sat 9/6/12</b>	<b>All</b>	<b>0%</b>		
19		Make updates to wiki page	8 days	Sun 10/6/12	Mon 18/6/12	Yi Zao, Zheng Keli	95%		

Project: Project Schedule Team Si  
Date: Sat 21/7/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names	% Complete		
								F	S
20		Discuss final adjustments of project scope with Masami (Email)	1 day	Mon 11/6/12	Tue 12/6/12	Zhang Yingyue	100%		
21		Consolidation of final changes (in technically defined scope)	5 days	Wed 13/6/12	Mon 18/6/12	Zhang Yingyue,Larry	100%		
22		<b>Discussion of project plans and risks for the elaboration phase</b>	<b>0 days</b>	<b>Wed 13/6/12</b>	<b>Wed 13/6/12</b>	<b>All</b>	<b>0%</b>		
23		Project managers to make final adjustments to schedule, prepare resources, create risks profile for the elaboration phase	4 days	Thu 14/6/12	Mon 18/6/12	Jeffrey,Kevin	25%		
24		Prepare project proposal and review wiki page	1 day	Tue 19/6/12	Wed 20/6/12	Kevin,Jeffrey	100%		
25		<b>Milestone- Project Proposal</b>	<b>0 days</b>	<b>Wed 20/6/12</b>	<b>Wed 20/6/12</b>	<b>All</b>	<b>100%</b>		
26		Buffer Days	0 days	Wed 20/6/12	Wed 20/6/12	All	0%		
27		<b>Elaboration Phase (Iteration 2)</b>	<b>19 days</b>	<b>Thu 21/6/12</b>	<b>Tue 10/7/12</b>	<b>All</b>	<b>0%</b>		
28		Confirm Idea internally within the team	3 days	Wed 27/6/12	Sat 30/6/12	All	100%		
29		Identify the correct Mobile Environment to build upon	3 days	Sat 30/6/12	Tue 3/7/12	Jeffrey	100%		
30		Create Use Case Diagrams and Use Case Descriptions	3 days	Sat 30/6/12	Tue 3/7/12	Zhang Yingyue	100%		
31		Setup Of Environment	1.71 days	Tue 3/7/12	Wed 4/7/12	All	100%		
32		<b>Learning on the Android Development</b>	<b>8 days</b>	<b>Thu 5/7/12</b>	<b>Fri 13/7/12</b>	<b>All</b>	<b>0%</b>		
33		Functional Development	13 days	Thu 5/7/12	Wed 18/7/12	Jeffrey,Kevin,Zhang	0%		
34		UI Development	13 days	Thu 5/7/12	Wed 18/7/12	Yi Zao,Zheng Keli	0%		
35		Exchange of ideas between functional & UI team happen on 2 occasions on developing application				All	0%		
36		Internal team review on learning development, Masami's feedbacks	0 days	Thu 12/7/12	Thu 12/7/12	All	0%		

Project: Project Schedule Team Si  
Date: Sat 21/7/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names	% Complete		
								F	S
37		<b>Schedule For Functional Development Team</b>					<b>0%</b>		
38		<b>Development Documentation</b>	<b>5 days</b>	<b>Wed 18/7/12</b>	<b>Mon 23/7/12</b>	<b>Kevin,Zhang Yingy</b>	<b>0%</b>		
39		SQL Database data table	3 days	Wed 18/7/12	Sat 21/7/12	Kevin	0%		
40		1st Review by Masami on discussed proposal	0 days	Sun 8/7/12	Sun 8/7/12	All	100%		
41		<b>Schedule For UI Development Team</b>					<b>0%</b>		
42		Free Form Diary UI & Newsletter UI	1 day	Sun 8/7/12	Mon 9/7/12	Yi Zao,Zheng Keli	0%		
43		Administer UI (For Worthy Cause Admin to edit photo into various forms & B1G1 Admin to post good pictures on the B1G1 portal)	3 days	Wed 11/7/12	Sat 14/7/12	Yi Zao,Zheng Keli	0%		
44		Reward System UI	9 days	Sat 14/7/12	Mon 23/7/12	Yi Zao,Zheng Keli	0%		
45		Final Check by project manager on overall UI diagram	1 day	Sun 22/7/12	Mon 23/7/12	Kevin	0%		
46		UI Mockup 1st Review with Masami	0 days	Mon 23/7/12	Mon 23/7/12	Yi Zao,Zheng Keli	0%		
47		Review Of UI Mockup from 1st Review	4 days	Mon 23/7/12	Fri 27/7/12	Yi Zao	0%		
48		UI Mockup 2nd Review with Masami	0 days	Fri 27/7/12	Fri 27/7/12	Yi Zao,Zheng Keli	0%		
49		Review of UI Mockup from 2nd Review	3 days	Fri 27/7/12	Mon 30/7/12	Yi Zao	0%		
50		UI Mockup Final Review with Masami	0 days	Mon 30/7/12	Mon 30/7/12	Yi Zao,Zheng Keli	0%		
51		<b>Preparation + Rehearsal for Presentation</b>	<b>4 days</b>	<b>Wed 8/8/12</b>	<b>Sun 12/8/12</b>	<b>Jeffrey,Kevin,Zhan</b>	<b>0%</b>		
52		Prepare Powerpoint Slides	2 days	Wed 8/8/12	Fri 10/8/12	Yi Zao,Zhang Yingy	0%		
53		Updates to wiki page	1 day	Fri 10/8/12	Sat 11/8/12	Yi Zao	0%		
54		Final updates to project schedule, risk assessments, learning outcomes, development documents	2 days	Wed 8/8/12	Fri 10/8/12	Kevin	0%		
55		Check powerpoint slides and wiki page ready	1 day	Sat 11/8/12	Sun 12/8/12	Kevin	0%		
56		Mock up presentation with Masami	0 days	Sun 12/8/12	Sun 12/8/12	Jeffrey,Kevin,Zhang	0%		

Project: Project Schedule Team Si Date: Sat 21/7/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	


ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names	% Complete		
								F	S
57		Buffer Days	1 day	Sun 12/8/12	Mon 13/8/12		0%		
58		Acceptance Presentation	0 days	Tue 14/8/12	Tue 14/8/12	Jeffrey, Kevin, Zhang	0%		
59		Construction phase	136 days	Tue 17/7/12	Fri 30/11/12		0%		
60		Schedule For Functional Development Team					0%		
61		Development of "Capture Photo" & "Upload Photo" function	25 days	Tue 17/7/12	Sat 11/8/12	Jeffrey, Kevin	0%		
62		App Startup Splash Screen	4 days	Wed 18/7/12	Sun 22/7/12	Jeffrey, Kevin	0%		
63		Study on how to develop App Startup Splash	1 day	Wed 18/7/12	Thu 19/7/12	Jeffrey, Kevin, Zhang	0%		
64		Development of App Startup Screen	2 days	Thu 19/7/12	Sat 21/7/12	Jeffrey, Kevin	0%		
65		Debugging for App Startup Screen	1 day	Sat 21/7/12	Sun 22/7/12	Jeffrey, Kevin	0%		
66		Login Screen for various users	3 days	Sun 22/7/12	Wed 25/7/12	Jeffrey, Kevin	0%		
67		[Description] WC team members (Leads to m					0%		
68		Study on the development of the login screen	2 days	Sun 22/7/12	Tue 24/7/12	Jeffrey, Kevin	0%		
69		Creation of SQL database till Access Photo Feature Part 1	2 days	Tue 24/7/12	Thu 26/7/12	Kevin	0%		
70		Development of Login Screen for various user + Linkage to SQL Database	2 days	Tue 24/7/12	Thu 26/7/12	Jeffrey	0%		
71		Debugging for Login Screen	1 day	Thu 26/7/12	Fri 27/7/12	Jeffrey, Kevin, Zhang	0%		
72		Main Menu For Users	6 days	Fri 27/7/12	Thu 2/8/12	Jeffrey, Kevin	0%		
73		[Description] Navigation to photo features & Capture Photo using Application					0%		
74		Study on the development of Main Menu For Users	2 days	Fri 27/7/12	Sun 29/7/12	Jeffrey, Kevin, Zhang Yingyue	0%		
75		Development of Main menu For Users	3 days	Sun 29/7/12	Wed 1/8/12	Jeffrey	0%		

Project: Project Schedule Team Si Date: Sat 21/7/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names	% Complete		
								F	S
76		Navigation to Photo features	2 days	Sun 29/7/12	Tue 31/7/12	Jeffrey	0%		
77		Capture Photo using Application	1 day	Tue 31/7/12	Wed 1/8/12	Jeffrey, Kevin	0%		
78		Debugging for Users main menu	2 days	Wed 1/8/12	Fri 3/8/12	Jeffrey, Kevin, Zhang	0%		
79		<b>Access Photo Feature (Part 1)</b>	5 days	Fri 3/8/12	Wed 8/8/12	Jeffrey	<b>0%</b>		
80		[Description]Entry Fields (Photo, Photo title, Photo description, GPS Location) & Actions: Snap, cancel & retake, delete, upload					0%		
81		Study the development of "Access Photo Features"					0%		
82		<b>Development of Access Photo Features</b>	<b>5 days</b>	<b>Fri 3/8/12</b>	<b>Wed 8/8/12</b>	<b>Jeffrey</b>	<b>0%</b>		
83		Actions: Snap, cancel, delete, upload	2 days	Fri 3/8/12	Sun 5/8/12	Jeffrey	0%		
84		Photo, Photo Title, Photo Description	1 day	Sun 5/8/12	Mon 6/8/12	Jeffrey	0%		
85		Debugging for Access Photo Feature	2 days	Mon 6/8/12	Wed 8/8/12	Jeffrey, Zhang Ying	0%		
86		<b>Schedule For UI Development Team</b>					<b>0%</b>		
87		UI Development for App Startup Splash and Login Screen	8 days	Tue 17/7/12	Wed 25/7/12	Zheng Keli	0%		
88		UI Development for Main Menu for Users	7 days	Fri 27/7/12	Fri 3/8/12	Zheng Keli	0%		
89		UI Development for Access Photo Feature	5 days	Fri 3/8/12	Wed 8/8/12	Yi Zao, Zheng Keli	0%		
90		Debugging for the overall functional application built so far	2 days	Wed 8/8/12	Fri 10/8/12	Jeffrey, Zheng Keli	0%		


Project: Project Schedule Team Si  
Date: Sat 21/7/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

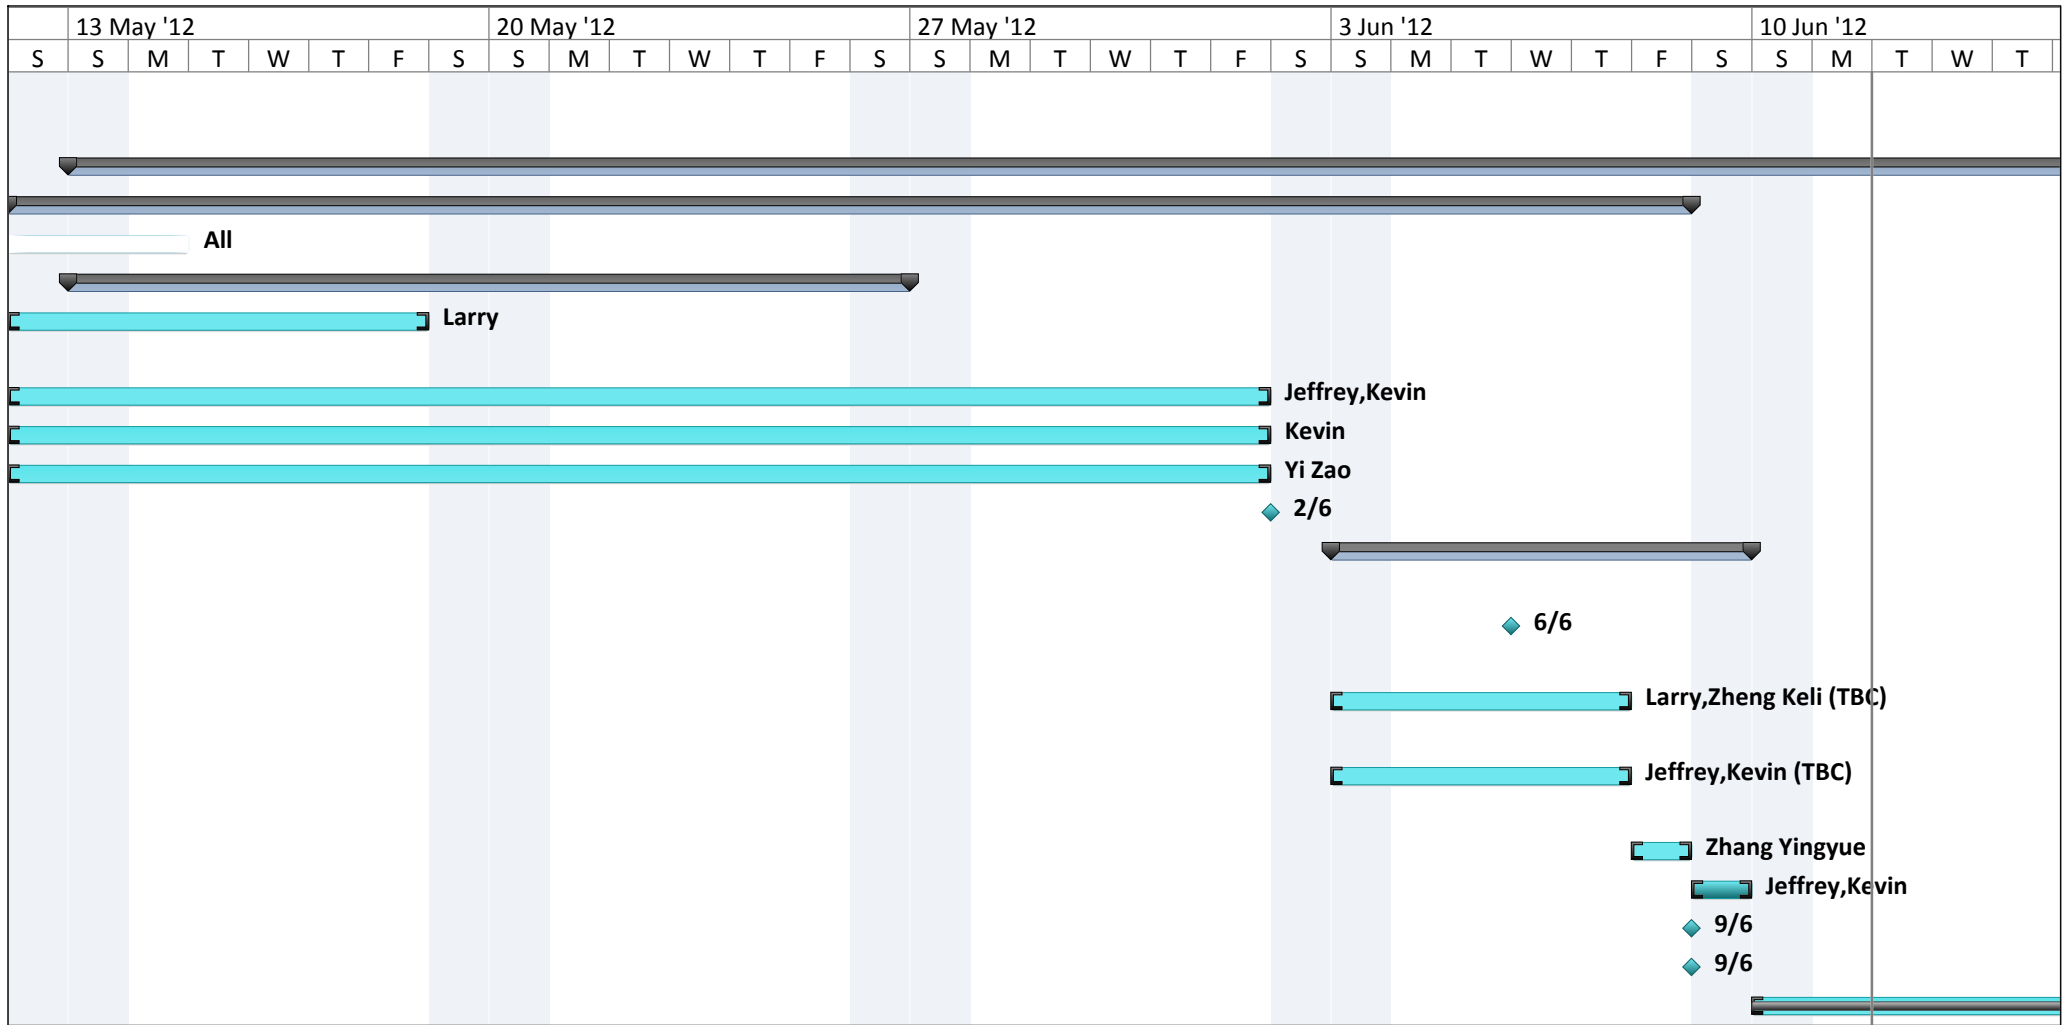





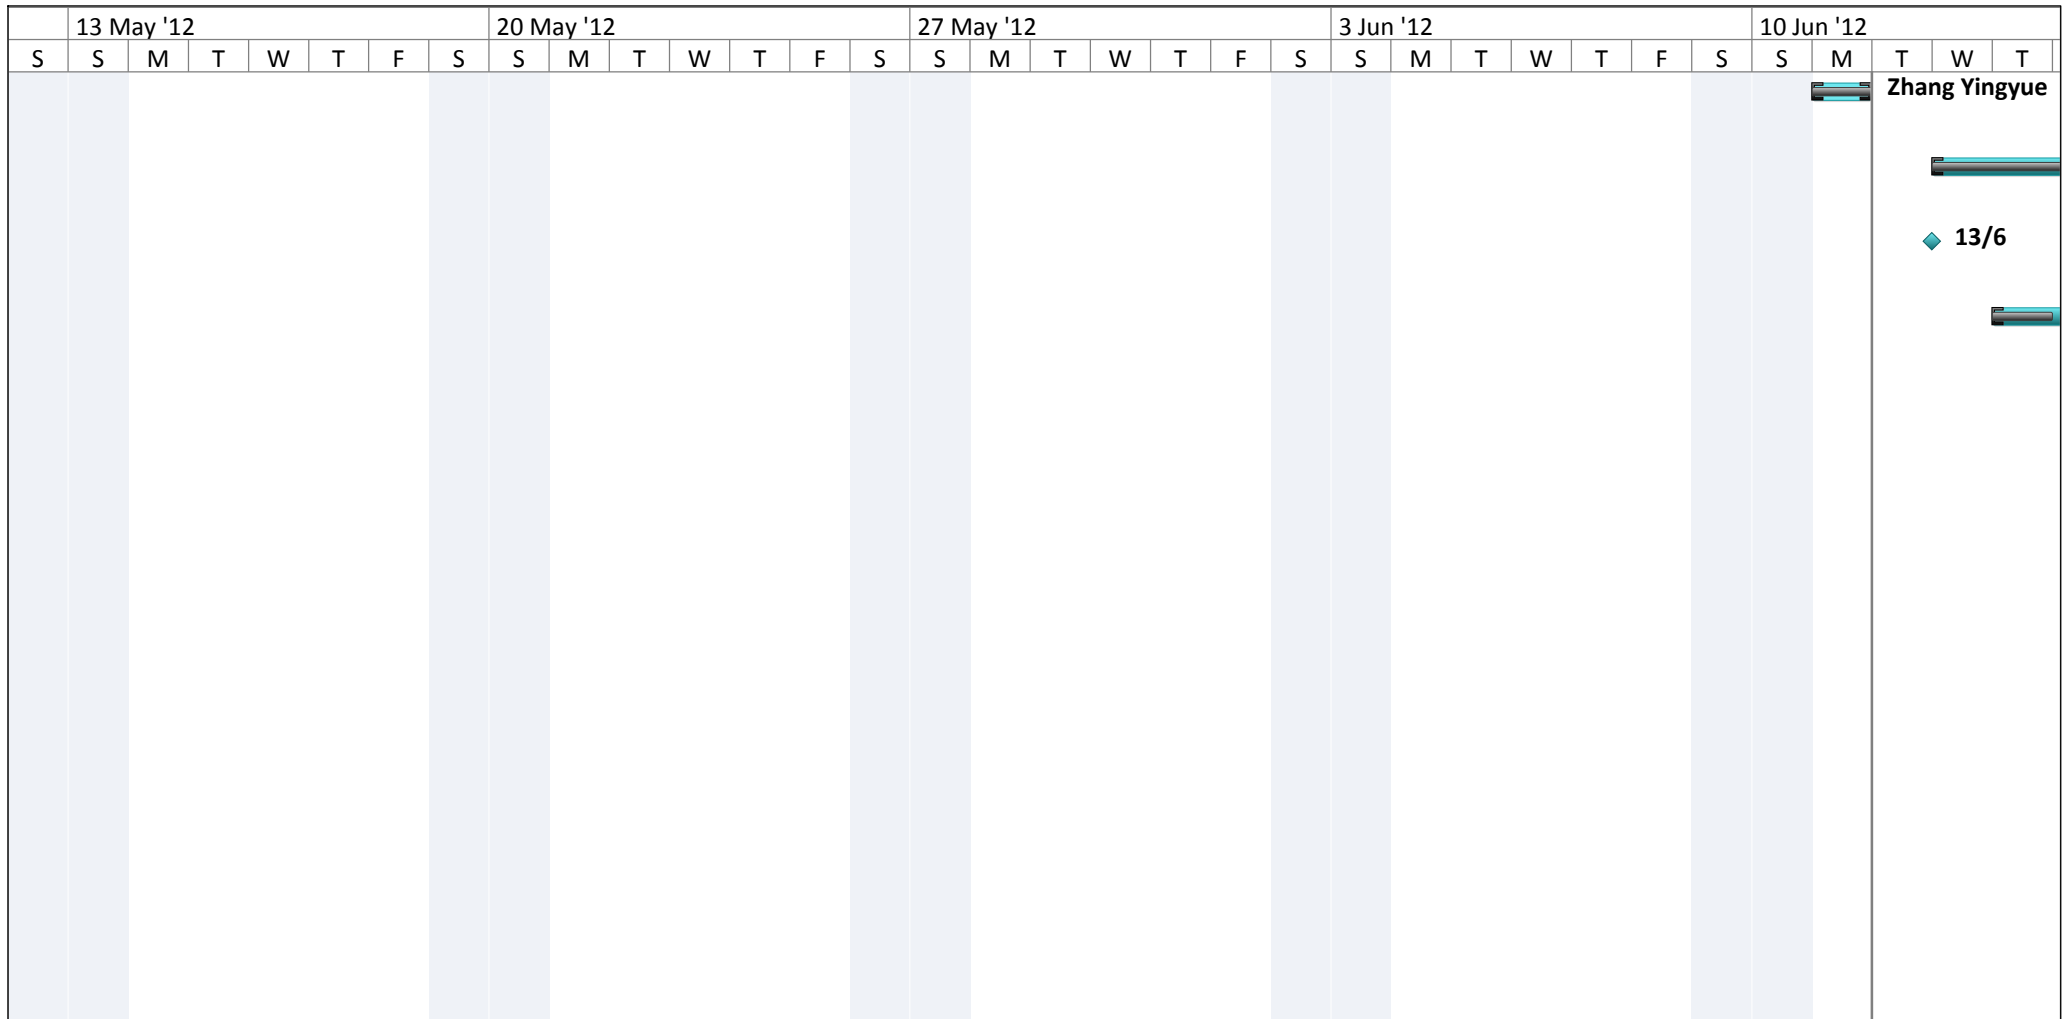










Project: Project Schedule Team Si  
Date: Sat 21/7/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	





















Project: Project Schedule Team Si  
Date: Sat 21/7/12


Task		External Milestone	◆	Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone	◆	Inactive Milestone	◆	Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	↓
External Tasks		Duration-only		Progress	





















Project: Project Schedule Team Si  
 Date: Sat 21/7/12



Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	





Project: Project Schedule Team Si  
Date: Sat 21/7/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	



Project: Project Schedule Team Si Date: Sat 21/7/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	
