

Supervisor Meeting

7th Feb 2014

Content

- Progress Update
- Schedule Update
- Task Breakdown
- Demo of Features

Progress Update

- Purpose Driven and Mastery-based Coaching
 - **High Priority now** – next Monday, Client meeting with IDA
 - Web Service will be provided by Client
 - Client request for admin page for Purpose driven and MB Coaching
 - Client wants different data structure – New data structure requires new logic
 - Debugged previous FYP code which allows MB coaching to work locally but did not debug other functions that did not affect out work directly (i.e. Mastery-based coaching works locally but did not debug his Practice play page)
 - **Client's E-mail @ 12 PM:**
 - Requesting for State Diagram that showcases coaching logic and transitions
 - Requesting team to come up with image and audio files (either by team or hire professional services) – Client will provide funding
 - Team has yet to decide follow-up action

Progress Update

- Purpose Driven and Mastery-based Coaching
 - Emphasized to client that admin page is a change in requirements although client thinks otherwise
 - Completed an admin page for purpose driven (had a personal version for debugging beforehand, 1 day taken) and client approves .
 - Mentioned to client that admin page for MB Coaching will take more time as it required different API and logic – **will not be considered** and did not promise client it will be
 - – Client decided to put admin coaching on hold
 - Yousof need to do up the state diagram on his functions before so that client will deploy – **notified today at 12 PM**. Client wants

Progress Update


- Tournament
 - Manage Tournament not completed
 - Bottleneck – WC was supposed to be assisting them.
 - Fariq now part of Tournament development group
 - Only APIs need to be completed for rest (Create, Join, Manage, Live Ranking, Mentor Assignment)– need to meet client next week
 - Entire Tournament function will be completed by 19th Feb, 2014
- Events Registration
 - Delay by 1.5 weeks – bottleneck
 - Still need to include loading and cut-off divider
 - Will be completed by tonight
- Map Registration
 - Client looking into fixing the function
 - Client removed deployment of map which was completed during acceptance

Progress Update

- User Testing 1
 - Proposed Date: 11th Feb 2014 (instead of 15th Feb 2014 – more users available on weekday)
 - Time: 0900-1600
 - Venue: SIS GSR
 - Functions to be tested:
 - Mastery Coaching
 - Purpose Driven
 - Events Registration
 - Heuristic

Schedule Update

- Status: **Behind Schedule**
- Current Iteration: 6

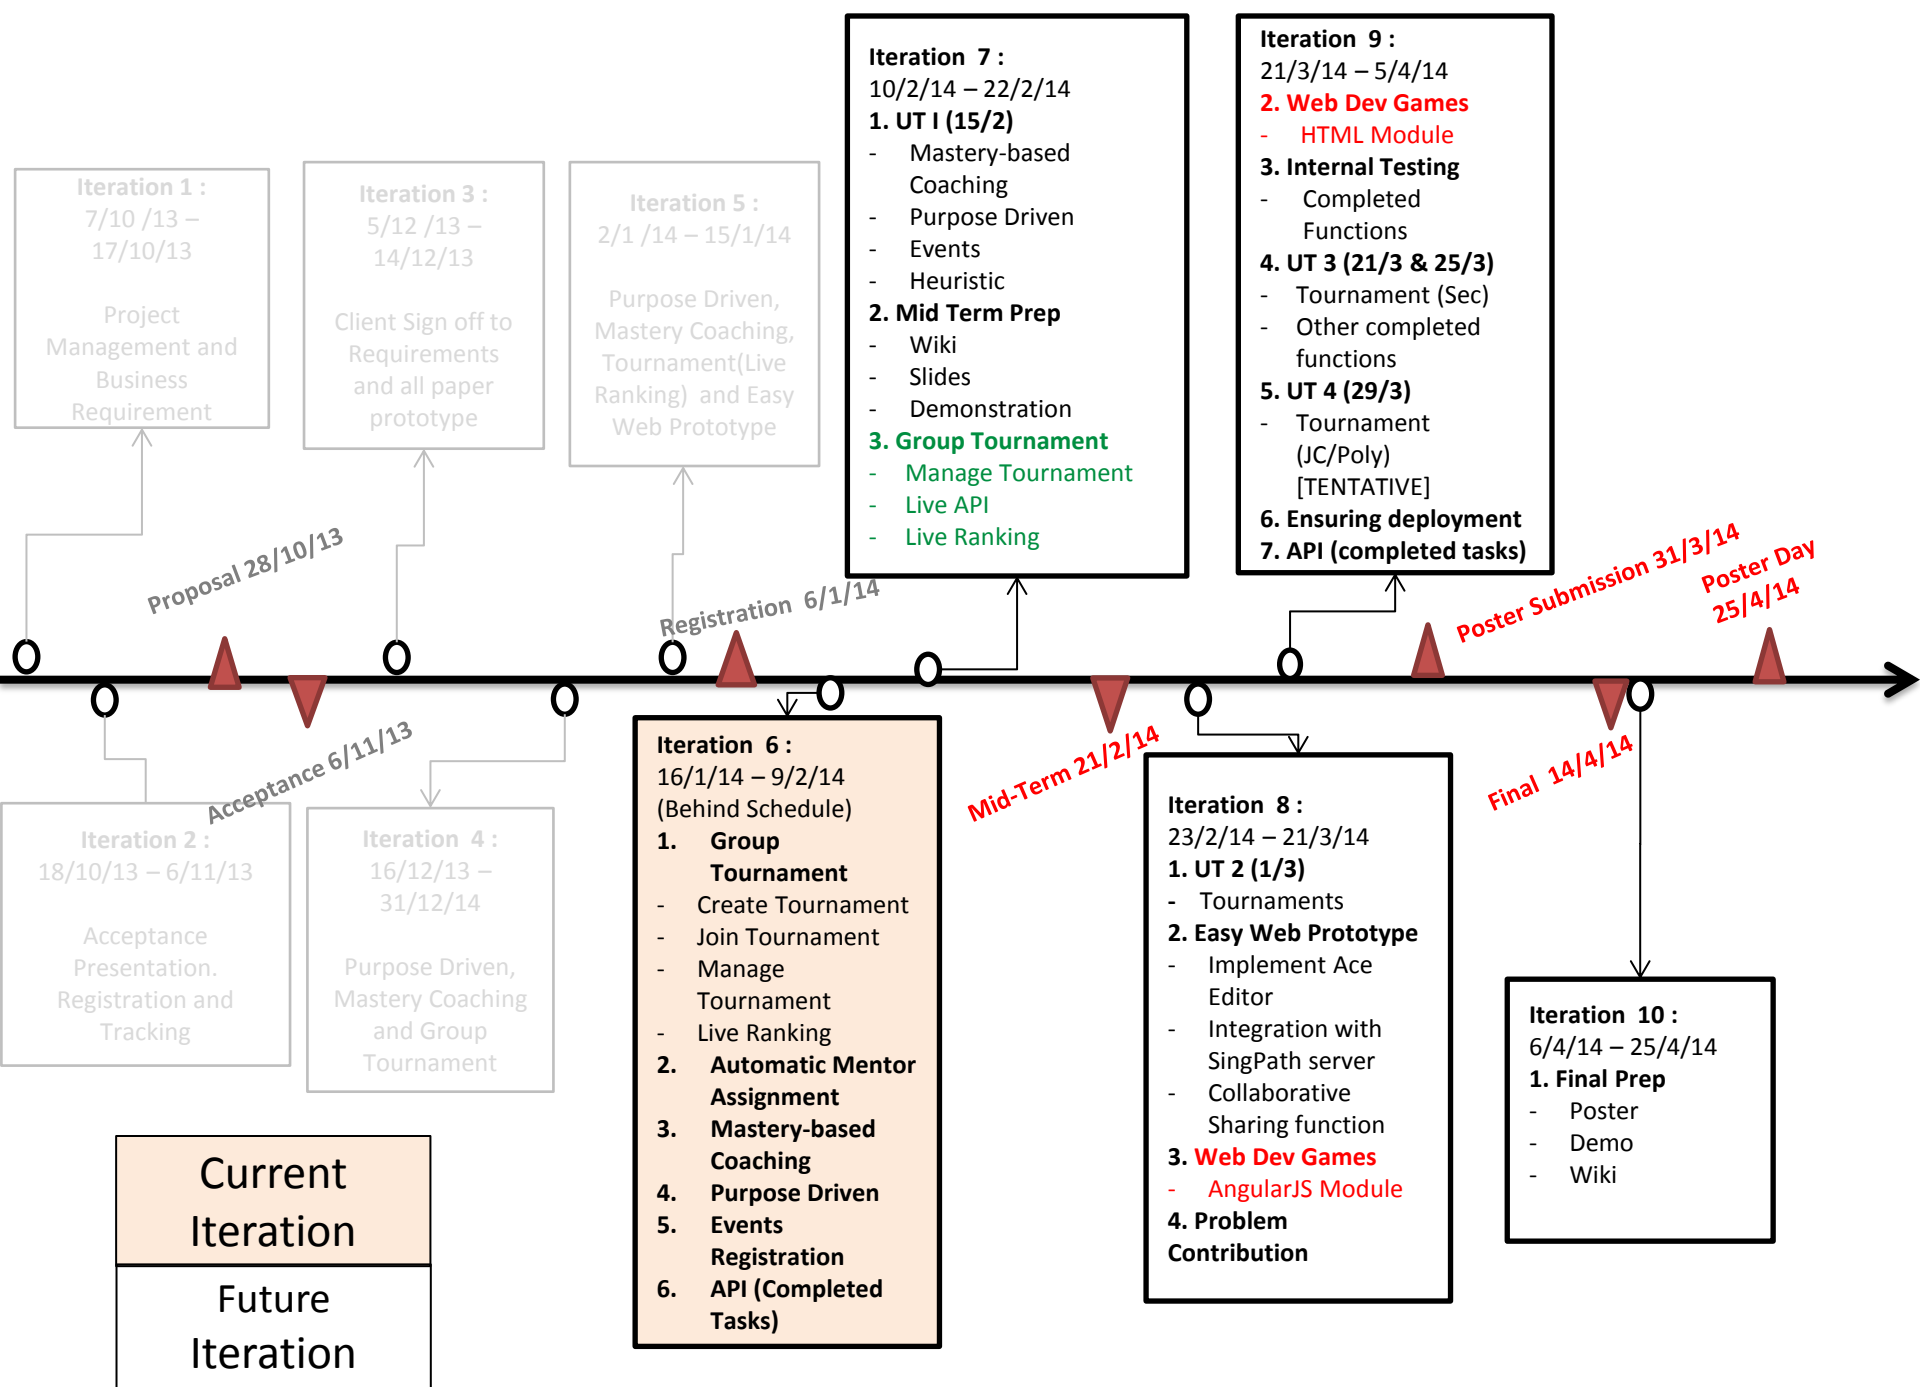

Task Breakdown

Official Role	Name	Allocated Task (Past)	Allocated Task (Upcoming)
Project Manager	Yousof	API for MB Coaching and Purpose Driven Test Case (Purpose Driven) Wiki	Mid Term Prep State diagrams (Purpose Driven) Debugging after UT
Business Analyst	Shanaaz	Test Case (MB Coaching) New home page Wiki (Assist on PM role)	Mid Term Prep API Document State Diagram (MB Coaching) Revamp Component diagram
Quality Assurance	Wah Chun	Events Test Cases (Events) Test Plan for UT	Events Oversee UT Assist in Mid Term Prep Automated Unit Testing
Lead UI/UX Developer	Fariq	Live Ranking Back end APIs for Tour	Tournament APIs
Co-Application Developer	Glen	Mentor Assignment Create , Manage & Join	Tournament APIs
Co-Application Developer	Eng Sen	Tournament	
