

ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
1			Note: 1 Day (Equivalent to 3 hours)				
2			Inception Phase	39 days	Sat 12/5/12	Wed 20/6/12	All
3			Idea Generation Phase	28 days	Sat 12/5/12	Sat 9/6/12	
4			Idea Discussion Meetings	3 days			All
5			Preliminary Idea Findings	14 days	Sat 12/5/12	Sat 26/5/12	
6			Get popularity Index feature and Internal Consulting Service	7 days	Sat 12/5/12	Sat 19/5/12	Larry
7			Worthy Cause Project- Match-Client	21 days	Sat 12/5/12	Sat 2/6/12	Jeffrey, Kevin
8			Reward System	21 days	Sat 12/5/12	Sat 2/6/12	Kevin
9			Share Worthy Cause project stories	21 days	Sat 12/5/12	Sat 2/6/12	Yi Zao
10			Feedback to Masami (Sponsor Meeting)	0 days	Sat 2/6/12	Sat 2/6/12	Zhang Yingyue
11			Change and Reviewed Idea Findings- Android Application	7 days	Sun 3/6/12	Sun 10/6/12	All
12			Discuss and confirm idea finding during sponsor meetings	0 days	Wed 6/6/12	Wed 6/6/12	All
13			Molecule Concept	5 days	Sun 3/6/12	Fri 8/6/12	Larry, Zheng Keli (T
14			Media Management Concept	5 days	Sun 3/6/12	Fri 8/6/12	Jeffrey, Kevin (TBC)
15			Consolidate All Ideas	1 day	Fri 8/6/12	Sat 9/6/12	Zhang Yingyue
16			Final Review by project managers	1 day	Sat 9/6/12	Sun 10/6/12	Jeffrey, Kevin
17			Start meeting with supervisor and Professor Zhu	0 days	Sat 9/6/12	Sat 9/6/12	All
18			Discussion of main plans for wiki page	0 days	Sat 9/6/12	Sat 9/6/12	All
19			Make updates to wiki page	8 days	Sun 10/6/12	Mon 18/6/12	Yi Zao, Zheng Keli
20			Discuss final adjustments of project scope with Masami (Email)	1 day	Mon 11/6/12	Tue 12/6/12	Zhang Yingyue
21			Consolidation of final changes (in technically defined scope)	5 days	Wed 13/6/12	Mon 18/6/12	Zhang Yingyue, Larr
22			Discussion of project plans and risks for the elaboration phase	0 days	Wed 13/6/12	Wed 13/6/12	All
23			Project managers to make final adjustments to schedule, prepare resources, create risks profile for the elaboration phase	4 days	Thu 14/6/12	Mon 18/6/12	Jeffrey, Kevin
24			Prepare project proposal and review wiki page	1 day	Tue 19/6/12	Wed 20/6/12	Kevin, Jeffrey

Project: Project Schedule Team Si Date: Thu 4/10/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

























ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
25			Milestone- Project Proposal	0 days	Wed 20/6/12	Wed 20/6/12	All
26			Buffer Days	0 days	Wed 20/6/12	Wed 20/6/12	All
27			Elaboration Phase	19 days	Thu 21/6/12	Tue 10/7/12	All
28			Confirm Idea internally within the team	3 days	Thu 21/6/12	Sun 24/6/12	All
29			Identify the correct Mobile Environment to build upon	3 days	Wed 27/6/12	Sat 30/6/12	Jeffrey
30			Create Use Case Diagrams and Use Case Descriptions	3 days	Sat 30/6/12	Tue 3/7/12	Zhang Yingyue
31			Setup Of Environment	1 day	Tue 3/7/12	Wed 4/7/12	All
32			Learning on the Android Development	8 days	Thu 5/7/12	Fri 13/7/12	All
33			Functional Development	13 days	Thu 5/7/12	Wed 18/7/12	Jeffrey, Kevin, Zhang
34			UI Development	13 days	Thu 5/7/12	Wed 18/7/12	Yi Zao, Zheng Keli
35			Exchange of ideas between functional & UI team happen on 2 occasions on developing application				All
36			Internal team review on learning development, Masami's feedbacks	0 days	Thu 12/7/12	Thu 12/7/12	All
37			Schedule For Functional Development Team				
38			Development Documentation	16 days	Wed 18/7/12	Fri 3/8/12	Kevin, Zhang Yingyue
39			SQL Database data table	3 days	Wed 18/7/12	Sat 21/7/12	Kevin
40			Review of SQL Database data table	13 days	Sat 21/7/12	Fri 3/8/12	Kevin, Zhang Yingyue
41			1st Review by Masami on discussed proposal	0 days	Sun 8/7/12	Sun 8/7/12	All
42			Schedule For UI Development Team				
43			Free Form Diary UI & Newsletter UI	1 day	Sun 8/7/12	Mon 9/7/12	Zheng Keli
44			Administer UI (For Worthy Cause Admin to edit photo into various forms & B1G1 Admin to post good pictures on the B1G1 portal)	3 days	Wed 11/7/12	Sat 14/7/12	Zheng Keli
45			Reward System UI	9 days	Sat 14/7/12	Mon 23/7/12	Zheng Keli
46			Final Check by project manager on overall UI diagram	1 day	Sun 22/7/12	Mon 23/7/12	Kevin
47			UI Mockup 1st Review with Masami	0 days	Mon 23/7/12	Mon 23/7/12	Yi Zao, Zheng Keli



















Project: Project Schedule Team Si Date: Thu 4/10/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	




















ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
48			Review Of UI Mockup from 1st Review	8 days	Mon 23/7/12	Tue 31/7/12	Zheng Keli
49			UI Mockup 2nd Review with Masami	0 days	Tue 31/7/12	Tue 31/7/12	Yi Zao,Zheng Keli
50			Review of UI Mockup from 2nd Review	3 days	Tue 31/7/12	Fri 3/8/12	Zheng Keli
51			UI Mockup Final Review with Masami	0 days	Fri 3/8/12	Fri 3/8/12	Yi Zao,Zheng Keli
52			Preparation + Rehearsal for Presentation	4 days	Wed 8/8/12	Sun 12/8/12	Jeffrey,Kevin,Zhan
53			Prepare Powerpoint Slides	2 days	Wed 8/8/12	Fri 10/8/12	Yi Zao,Zhang Yingy
54			Updates to wiki page	1 day	Fri 10/8/12	Sat 11/8/12	Yi Zao
55			Final updates to project schedule, risk assessments, learning outcomes, development documents	2 days	Wed 8/8/12	Fri 10/8/12	Kevin
56			Check powerpoint slides and wiki page ready	1 day	Sat 11/8/12	Sun 12/8/12	Kevin
57			Buffer Days	1 day	Sun 12/8/12	Mon 13/8/12	
58			Acceptance Presentation	0 days	Tue 14/8/12	Tue 14/8/12	Jeffrey,Kevin,Zhang
59			Construction phase (Iteration 1 to 8)	125 days	Tue 24/7/12	Mon 26/11/12	
60			Iteration 1- Manage Photo Part 1 (Take Photo with App, App Splash Page, Login)	17 days	Tue 24/7/12	Fri 10/8/12	
61			Schedule For Functional Development Team				
62			Development of "Capture Photo" & "Upload Photo" function	27 days	Tue 31/7/12	Mon 27/8/12	Jeffrey,Kevin
63			App Startup Splash Screen	4 days	Wed 18/7/12	Sun 22/7/12	Jeffrey,Kevin
64			Study on how to develop App Startup Splash	1 day	Wed 18/7/12	Thu 19/7/12	Jeffrey,Kevin,Zhang
65			Development of App Startup Screen	2 days	Thu 19/7/12	Sat 21/7/12	Jeffrey,Kevin
66			Debugging for App Startup Screen	1 day	Sat 21/7/12	Sun 22/7/12	Jeffrey,Kevin
67			Login Screen for various users	1 day	Tue 7/8/12	Wed 8/8/12	Kevin
68			[Description] WC team members (Leads to main menu), B1G1 businesses (Leads to web portal)				
69			Study on the development of the login screen	0.5 days	Tue 7/8/12	Tue 7/8/12	Kevin

Project: Project Schedule Team Si
Date: Thu 4/10/12



















Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
70			Creation of SQL database till Access Photo Feature Part 1	1 day	Tue 7/8/12	Wed 8/8/12	Kevin
71			Development of Login Screen for various user + Linkage to SQL Database	2 days	Tue 24/7/12	Thu 26/7/12	Zheng Keli
72			Debugging for Login Screen	1 day	Thu 26/7/12	Fri 27/7/12	Zheng Keli
73			Access Photo Feature	5 days	Fri 3/8/12	Wed 8/8/12	Jeffrey
74			[Description]Entry Fields (Photo, Photo title, Photo description, GPS Location) & Actions: Snap, cancel & retake, delete, upload	1 day	Fri 3/8/12	Sat 4/8/12	
75			Study the development of "Access Photo Features"	1 day	Fri 3/8/12	Sat 4/8/12	
76			Development of Access Photo Features	5 days	Fri 3/8/12	Wed 8/8/12	Jeffrey
77			Actions: Snap, cancel, delete, upload	1 day	Fri 3/8/12	Sat 4/8/12	Jeffrey
78			Photo preview from photo library	1 day	Sat 4/8/12	Sun 5/8/12	Jeffrey
79			Photo, Photo Title, Live Feed Update	1 day	Sun 5/8/12	Mon 6/8/12	Jeffrey
80			Debugging for Access Photo Feature	2 days	Mon 6/8/12	Wed 8/8/12	Jeffrey,Zheng Keli
81			Schedule For UI Development Team				
82			UI Development for App Startup Splash and Login Screen	8 days	Tue 17/7/12	Wed 25/7/12	Zheng Keli
83			UI Development for Access Photo Feature	5 days	Fri 3/8/12	Wed 8/8/12	Yi Zao,Zheng Keli
84			Debugging for the overall functional application built so far	2 days	Wed 8/8/12	Fri 10/8/12	Jeffrey,Zheng Keli
85			Iteration 2 - Manage Photo Part 2 (Image Cropping, Image Filtering to be displayed photo in diary entry)	14 days	Sun 19/8/12	Sun 2/9/12	
86			Development Of Photo Cropping and Photo Filtering function	14 days	Sun 19/8/12	Sun 2/9/12	
87			Study how to develop the photo cropping and filtering function for the photo just added to the application	3 days	Sun 19/8/12	Wed 22/8/12	All
88			Prepare Test cases for Photo Cropping and filter function	1.5 days	Wed 22/8/12	Thu 23/8/12	Zhang Yingyue
89			Schedule for Functional Development Team				

Project: Project Schedule Team Si Date: Thu 4/10/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
90			Crop the original photo taken into any size or dimensions the users see fit	4 days	Wed 22/8/12	Sun 26/8/12	Jeffrey, Kevin
91			After the rectangle is displayed, the unselected area should be cropped	4 days	Wed 22/8/12	Sun 26/8/12	Jeffrey, Kevin
92			Ensure the original photo is retained in the database and the cropped photo is added				
93			Schedule for UI Development Team				
94			Page setup of displaying the picture on a new page in the Android application	1 day	Mon 20/8/12	Tue 21/8/12	Zheng Keli, Yi Zao
95			Create the rectangle to indicate the area of effect of the picture that the user wants preserved after cropping	1 day	Tue 21/8/12	Wed 22/8/12	Yi Zao, Zheng Keli
96			Create the filtering feature on the photo	4 days	Wed 22/8/12	Sun 26/8/12	Yi Zao, Zheng Keli
97			Debugging for the Photo Cropping Function	2 days	Mon 27/8/12	Wed 29/8/12	Jeffrey, Kevin
98			Debugging For Photo Filter function	1.5 days	Wed 29/8/12	Thu 30/8/12	Jeffrey, Zheng Keli
99			Buffer Days	2 days			
100			Iteration 3 - Manage Diary Entry Part 1(View Live Feed & Search Location)	13 days	Sun 2/9/12	Sat 15/9/12	
101			Development of live feed function	6 days	Sun 2/9/12	Sat 8/9/12	
102			Learn how to populate the live feeds on the "Special Moments" page and enable the worthy cause admin from the Drupal site to see into these live feeds + further requirements gathering (how the list is going to populate)	2 days	Sun 2/9/12	Tue 4/9/12	All
103			Prepare test cases for "Live Feed" function	1 day	Tue 4/9/12	Wed 5/9/12	Zhang Yingyue
104			Schedule for Functional Development Team				
105			Populate the live updates accordingly for the "Special Moments" page in the app	4 days	Tue 4/9/12	Sat 8/9/12	




Project: Project Schedule Team Si
Date: Thu 4/10/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	



















ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names
106		As more live feeds are added, populate the lists in the appropriate order and length in the page as decided by the sponsor	1 day	Tue 4/9/12	Wed 5/9/12	Jeffrey
107		Schedule for UI development team				
108		Embolden words, decorate and format accurately the "Special Moments" page	1 day	Tue 4/9/12	Wed 5/9/12	Yi Zao,Zheng Keli
109		Debugging for View Live Feed Function	3 days	Wed 5/9/12	Sat 8/9/12	Jeffrey,Zheng Keli,
110		Development of Search Location feature	7 days	Sat 8/9/12	Sat 15/9/12	
111		Learn how to retrieve coordinates from the Android phone using an application and then query the coordinates using Google API	2 days	Sat 8/9/12	Mon 10/9/12	All
112		Prepare test cases for the Search Location feature	1 day	Mon 10/9/12	Tue 11/9/12	Zhang Yingyue
113		Schedule for Functional Development Team				
114		Display the location name using the Google API and coordinates given by the GPS on the diary entry page	4 days	Tue 11/9/12	Sat 15/9/12	Jeffrey,Kevin
115		Schedule for UI Development Team				
116		(Optional Requirement- to discuss with Masami) Develop the google map on B1G1 app indicating the precise locaton given by the GPS	3 days	Mon 10/9/12	Thu 13/9/12	Yi Zao,Zheng Keli
117		Debugging for Search Location feature	2 days	Thu 13/9/12	Sat 15/9/12	
118		Iteration 4 - Storage of diary entry descriptions into the B1G1 database	13 days	Sat 15/9/12	Fri 28/9/12	
119		Research on methods to store information to database and find out more information about storage to image	3 days	Sat 15/9/12	Tue 18/9/12	
120		Uploading large and small images to personal library in phone (SD Card)	3 days	Tue 18/9/12	Fri 21/9/12	Jeffrey,Zheng Keli
121		Uploading of image title, description, location, and project to the database	4 days	Fri 21/9/12	Tue 25/9/12	Zheng Keli,Jeffrey
122		Buffer days	3 days	Tue 25/9/12	Fri 28/9/12	


























Project: Project Schedule Team Si
Date: Thu 4/10/12



















Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	








































ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
123			Milestone 3 - UT 1	7 days	Sat 22/9/12	Sat 29/9/12	Kevin,Yi Zao,Zhang
124			Preparation for Mid-Term Presentation	4 days	Sun 30/9/12	Thu 4/10/12	Kevin,Yi Zao,Zhang
125			Mid-Term structure + slides	2 days	Sun 30/9/12	Tue 2/10/12	Kevin,Yi Zao,Zhang
126			Rehearsal of individual parts	2 days	Tue 2/10/12	Thu 4/10/12	All
127			Milestone 4 - Mid Term Presentation	0 days	Thu 4/10/12	Thu 4/10/12	All
128			Iteration 5 - Manage Diary Entry Part 2 (Live Feed Sharing on Twitter & Facebook, Implement live feed and photo on web portal)	11 days	Thu 4/10/12	Mon 15/10/12	
129			Learn about facebook & twitter API to post the live feed from the app to facebook or twitter + method to populate live updates + Store Photo in Web Portal + final requirements gathering on this function	1.5 days	Thu 4/10/12	Fri 5/10/12	All
130			Prepare test cases for "Live Feed Sharing" function	1 day	Fri 5/10/12	Sat 6/10/12	Zhang Yingyue
131			Schedule for Functional Development Team				
132			Uploading image from personal library to B1G1 portal & generate its url	2 days	Sat 6/10/12	Mon 8/10/12	Jeffrey,Zheng Keli
133			Populate the live updates in the WC Admin Home Page	5 days	Fri 5/10/12	Wed 10/10/12	Kevin
134			Display the live feed on facebook- Integration with mobile app and facebook	1.5 days	Mon 8/10/12	Tue 9/10/12	Jeffrey
135			Display the live feed on twitter - Integrating mobile app with twitter	1.5 days	Wed 10/10/12	Thu 11/10/12	Jeffrey
136			Schedule for UI Development Team				
137			Create css files to ensure the slide function is implemented in the WC Admin Home Page for the live feed updates	3 days	Fri 5/10/12	Mon 8/10/12	Zhang Yingyue
138			Prepare the pop-up options for the user to select where to upload their live feeds	2 days	Mon 8/10/12	Wed 10/10/12	Zheng Keli
139			Integrate the developments done by the UI & Functional development team	1 day	Wed 10/10/12	Thu 11/10/12	Jeffrey,Kevin,Zheng Keli
140			Debug for all functions in the iteration	2 days	Thu 11/10/12	Sat 13/10/12	Jeffrey,Kevin,Zhang



















Project: Project Schedule Team Si
Date: Thu 4/10/12



Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	 Task Mode	Task Name	Duration	Start	Finish	Resource Names
141		Buffer Days	2 days	Sat 13/10/12	Mon 15/10/12	
142		Iteration 6 - Manage WC Team Members	11 days	Mon 15/10/12	Fri 26/10/12	
143		Development of "Create & Access worthy cause team member accounts" function	11 days	Mon 15/10/12	Fri 26/10/12	
144	 	Learn to create user accounts and populate the user accounts under B1G1 Giving's Team Members	1.5 days	Mon 15/10/12	Tue 16/10/12	All
145		Prepare test cases for "Manage team members" function	1 day	Tue 16/10/12	Wed 17/10/12	Zhang Yingyue
146	 	Schedule For Functional Development Team				
147		Accept values from the create account fields and store it in the database	3 days	Tue 16/10/12	Fri 19/10/12	Kevin
148	 	Logic to retrieve the user accounts from the database and populate it on the "Manage Team Member's Page"	3 days	Fri 19/10/12	Mon 22/10/12	Kevin,Zheng Keli
149	 	Schedule for UI Development Team				
150		Develop the user interface for the "Create Accounts field"	2 days	Mon 15/10/12	Wed 17/10/12	Zheng Keli
151		Develop the user interface for the "B1G1 Giving's Team Members" Section	2 days	Wed 17/10/12	Fri 19/10/12	Zheng Keli
152	 	Develop the user interface for the rest of the "Manage team members" page	2 days	Fri 19/10/12	Sun 21/10/12	Zheng Keli
153		Debug for Manage WC Team Members function	2 days	Mon 22/10/12	Wed 24/10/12	Kevin,Zheng Keli
154		Buffer Days	1.5 days	Thu 25/10/12	Fri 26/10/12	
155		Iteration 7- Manage Projects	14 days	Fri 26/10/12	Fri 9/11/12	
156	 	Research on retrieving filtered list for top projects & least popular ones in drupal	2 days	Fri 26/10/12	Sun 28/10/12	Jeffrey, Kevin, Zheng Keli
157		Prepare test cases for "Manage team members" site	2 days	Sun 28/10/12	Tue 30/10/12	Zhang Yingyue
158		Schedule for Functional Development Team	9 days	Fri 26/10/12	Sun 4/11/12	



















Project: Project Schedule Team Si Date: Thu 4/10/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	


ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
159			Retrieve list of projects from B1G1 database to the drupal web-site	9 days	Fri 26/10/12	Sun 4/11/12	
160			Connect the drupal site to the B1G1 database and retrieve an instance of the project	1.5 days	Fri 26/10/12	Sat 27/10/12	Zheng Keli
161			Dynamically retrieve all projects from the B1g1 database	1.5 days	Sun 28/10/12	Mon 29/10/12	Kevin,Zheng Keli
162			Latest updates from diary entry	2 days	Mon 29/10/12	Wed 31/10/12	Kevin
163			Filter only top projects and least popular projects	1.5 days	Wed 31/10/12	Thu 1/11/12	Kevin,Zheng Keli
164			Ensure the order is correct for the top and least popular projects	0.5 days	Thu 1/11/12	Thu 1/11/12	Kevin,Zheng Keli
165			"Remove this project" function	1.5 days	Thu 1/11/12	Fri 2/11/12	Zheng Keli,Kevin
166			"Add new project" function	1.5 days	Sat 3/11/12	Sun 4/11/12	Kevin
167			Schedule for UI Development Team	5 days	Sat 27/10/12	Thu 1/11/12	
168			CSS Layout and organise structure for project list	3 days	Sat 27/10/12	Tue 30/10/12	Zheng Keli
169			CSS Layout for top projects and least popular projects	2 days	Fri 2/11/12	Sun 4/11/12	Zheng Keli
170			Debugging for Manage Projects	2 days	Sun 4/11/12	Tue 6/11/12	Kevin,Zheng Keli
171			Buffer Days	3 days	Tue 6/11/12	Fri 9/11/12	
172			Milestone 5 - UT 2	7 days	Fri 9/11/12	Fri 16/11/12	All
173			Transition Phase	17 days	Fri 16/11/12	Mon 3/12/12	All
174			Iteration 8 - UI touchup and final debugging	9 days	Fri 16/11/12	Sun 25/11/12	
175			Final Integration Of Codes	3 days	Fri 16/11/12	Mon 19/11/12	Jeffrey,Kevin
176			Debug entire application & testing	4 days	Mon 19/11/12	Fri 23/11/12	Jeffrey,Kevin
177			Make UI more consistent with the requirements of sponsor	5 days	Thu 15/11/12	Tue 20/11/12	Zheng Keli
178			Buffer Days	2 days	Fri 23/11/12	Sun 25/11/12	
179			Milestone 6 - UAT 1	0 days	Sun 25/11/12	Sun 25/11/12	All
180			Deployment to HockeyKit	2 days	Sun 25/11/12	Tue 27/11/12	Jeffrey,Kevin
181			Complete Deployment to the B1G1 Live Server	2 days	Sun 25/11/12	Tue 27/11/12	Kevin,Jeffrey
182			Final Project Presentations	6 days	Thu 29/11/12	Wed 5/12/12	

Project: Project Schedule Team Si Date: Thu 4/10/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
183			Preparation of project management documents	3 days	Thu 29/11/12	Sun 2/12/12	Jeffrey, Kevin
184			Prepare presentation slides	3 days	Thu 29/11/12	Sun 2/12/12	Yi Zao, Zhang Yingy
185			Prepare speech presentation	1 day	Sun 2/12/12	Mon 3/12/12	All
186			Buffer Days	1 day	Mon 3/12/12	Tue 4/12/12	
187			Milestone 7 - Final Presentation	1 day	Tue 4/12/12	Wed 5/12/12	
188			Prepare Poster for Poster Day	2 days	Wed 5/12/12	Fri 7/12/12	All
189			Milestone 8 - Poster Day	0 days	Fri 7/12/12	Fri 7/12/12	


Project: Project Schedule Team Si
Date: Thu 4/10/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

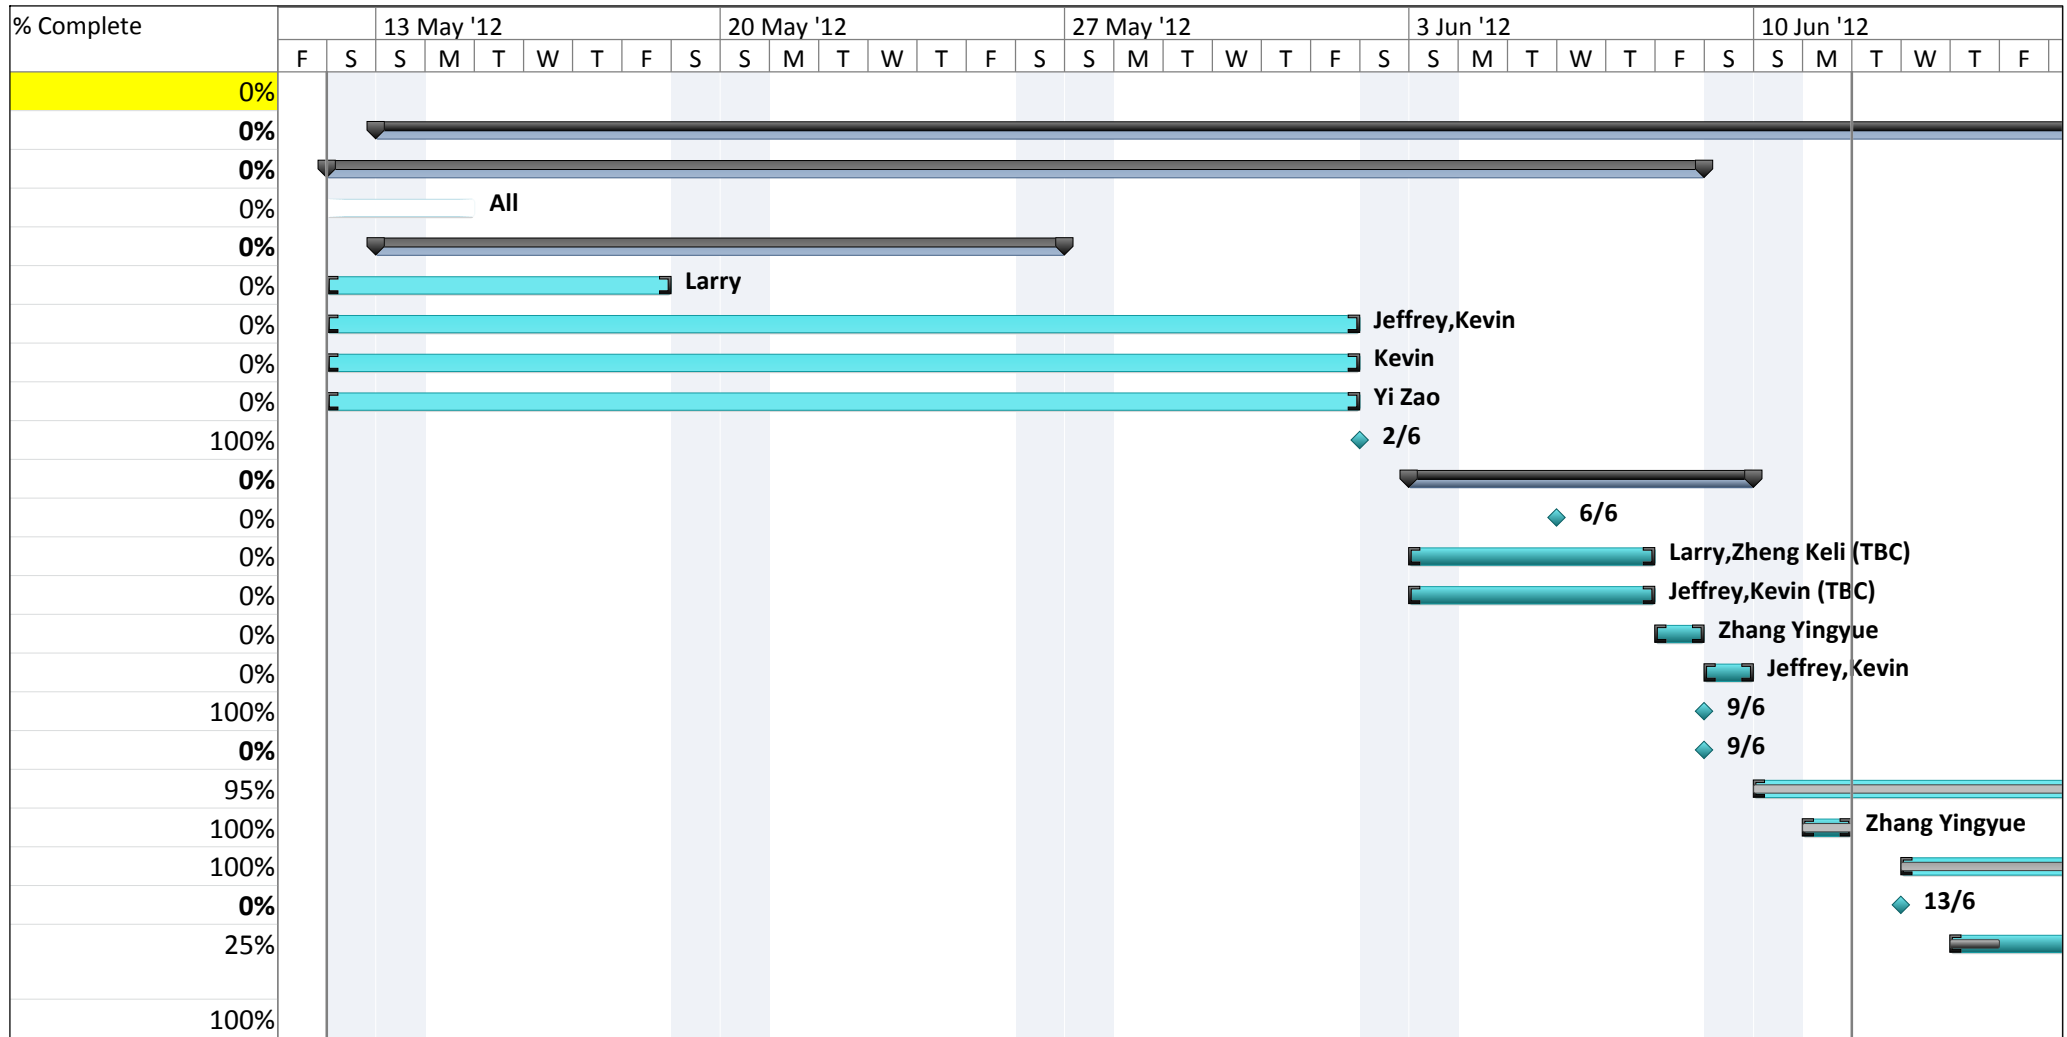


Project: Project Schedule Team Si
Date: Thu 4/10/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

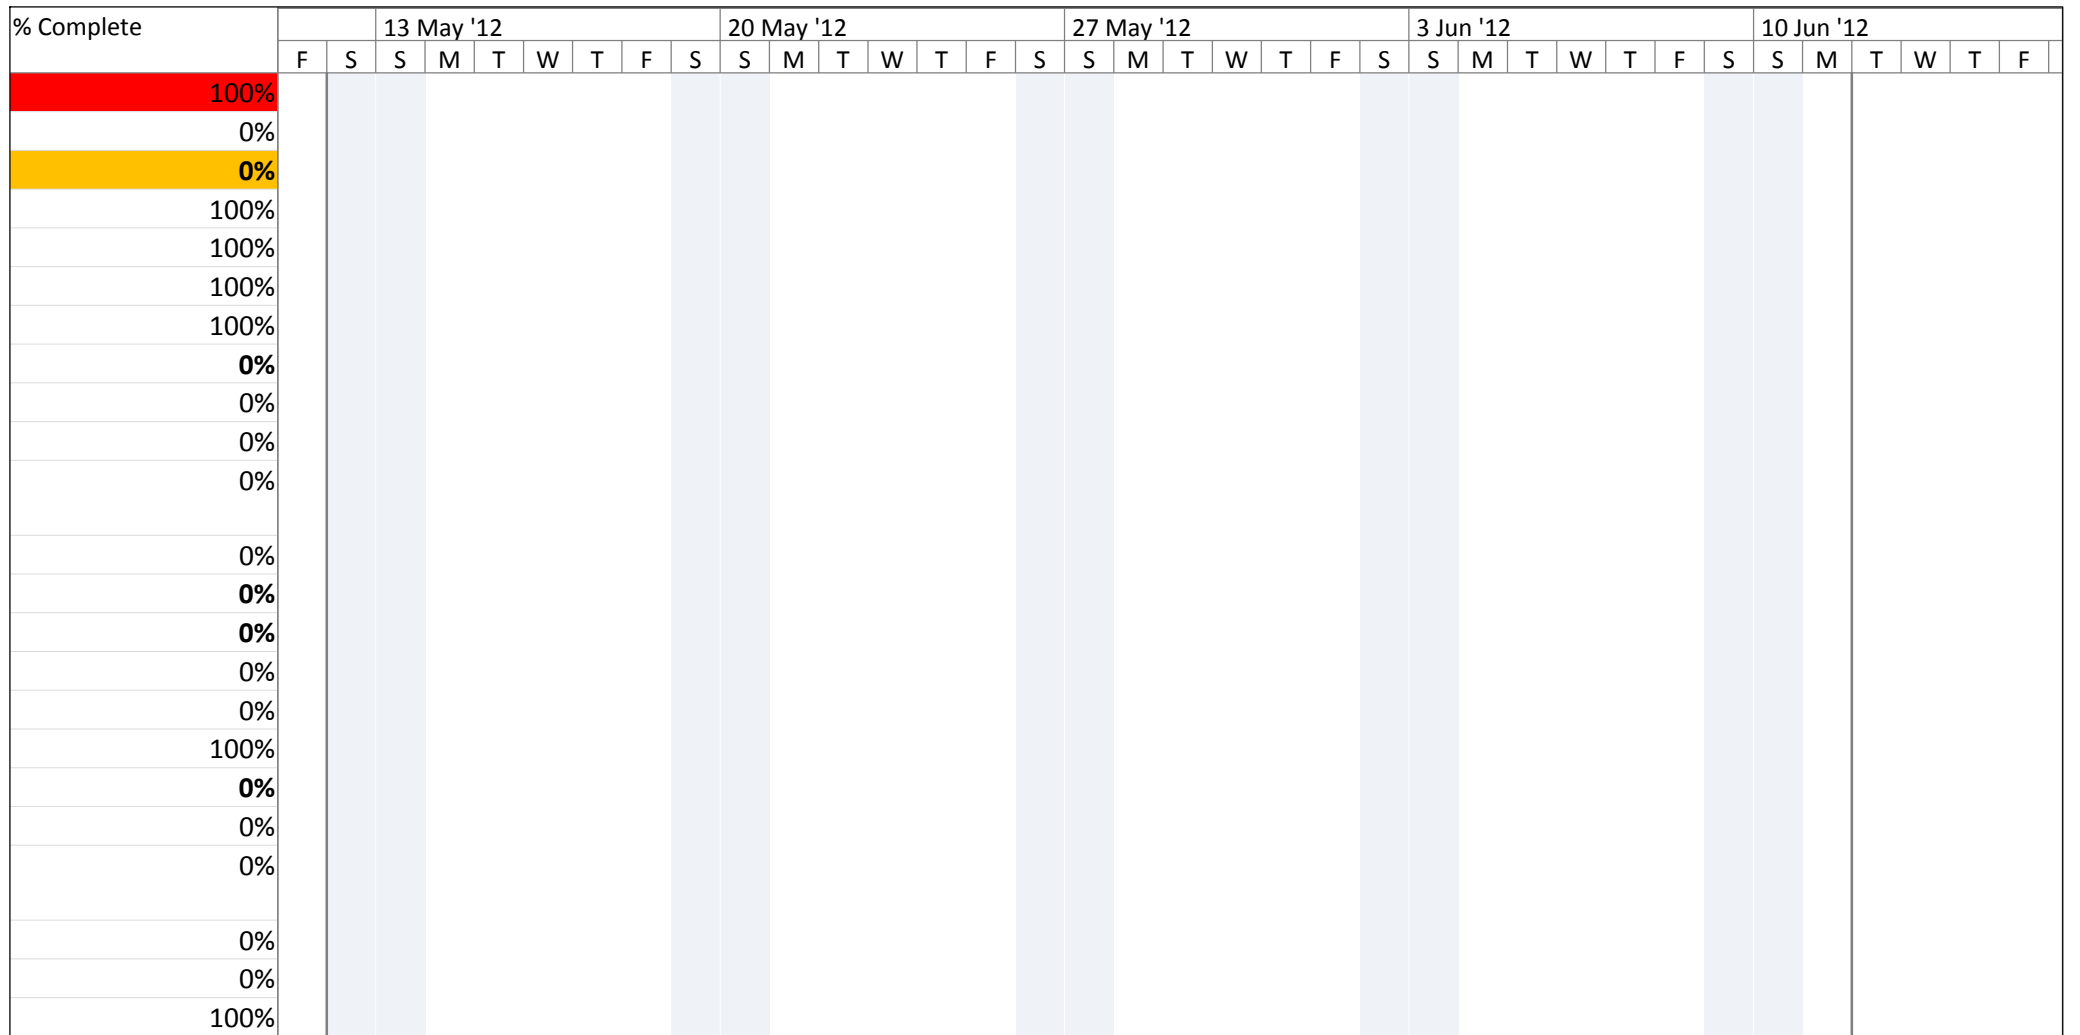


Project: Project Schedule Team Si
Date: Thu 4/10/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

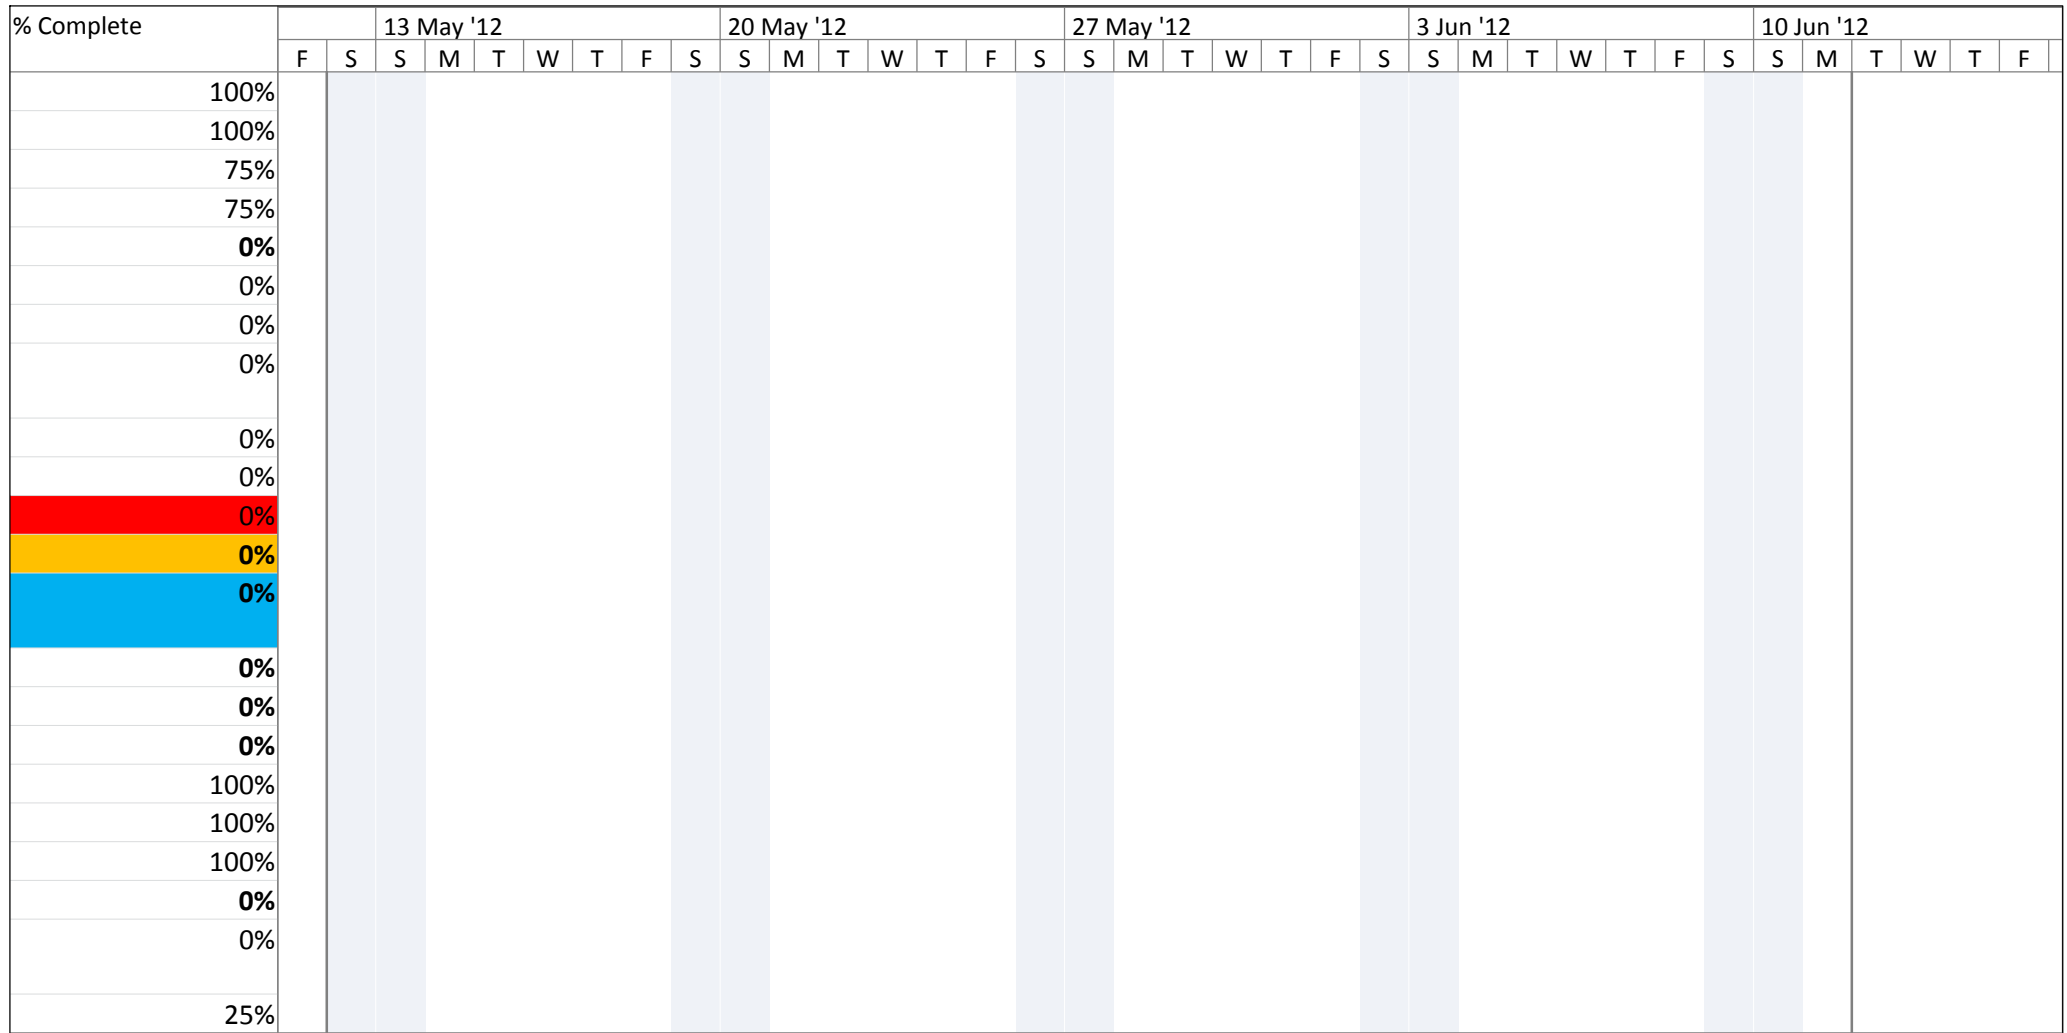


Project: Project Schedule Team Si
Date: Thu 4/10/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

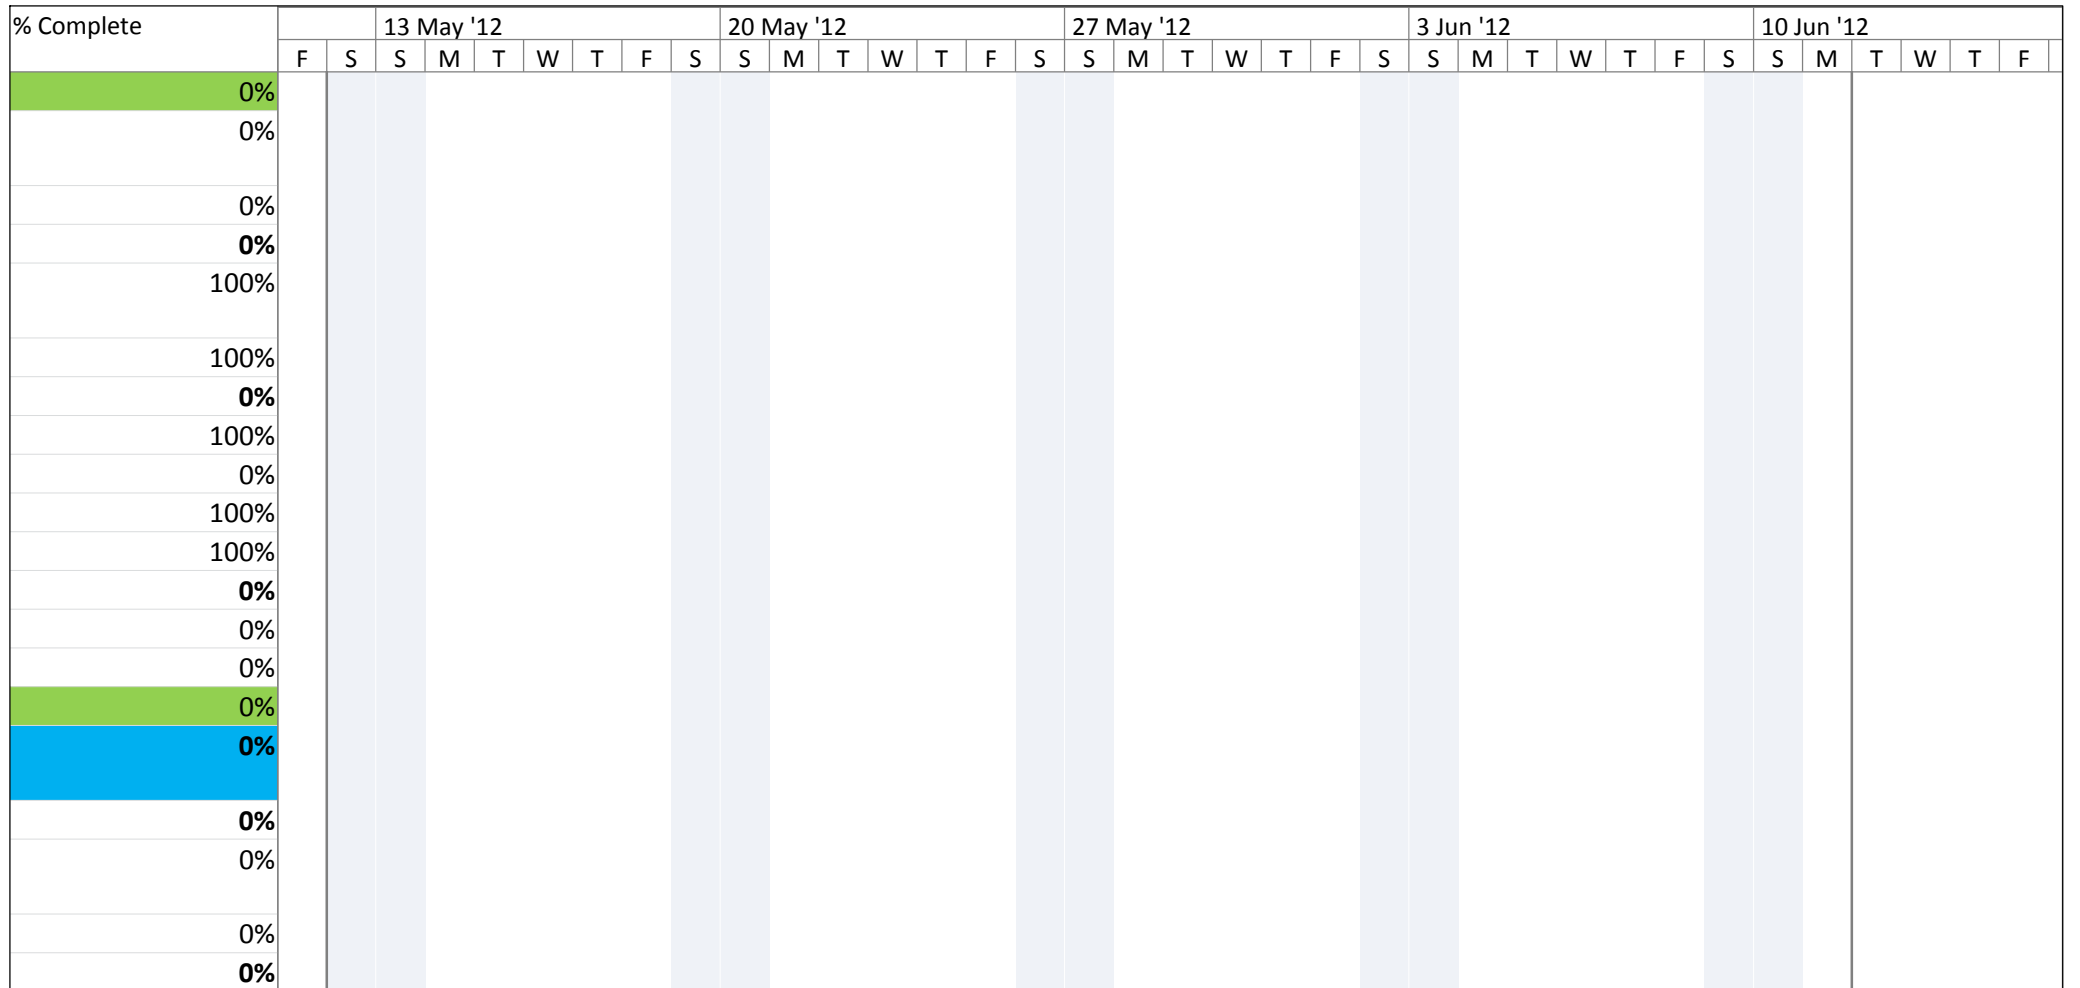

Project: Project Schedule Team Si Date: Thu 4/10/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

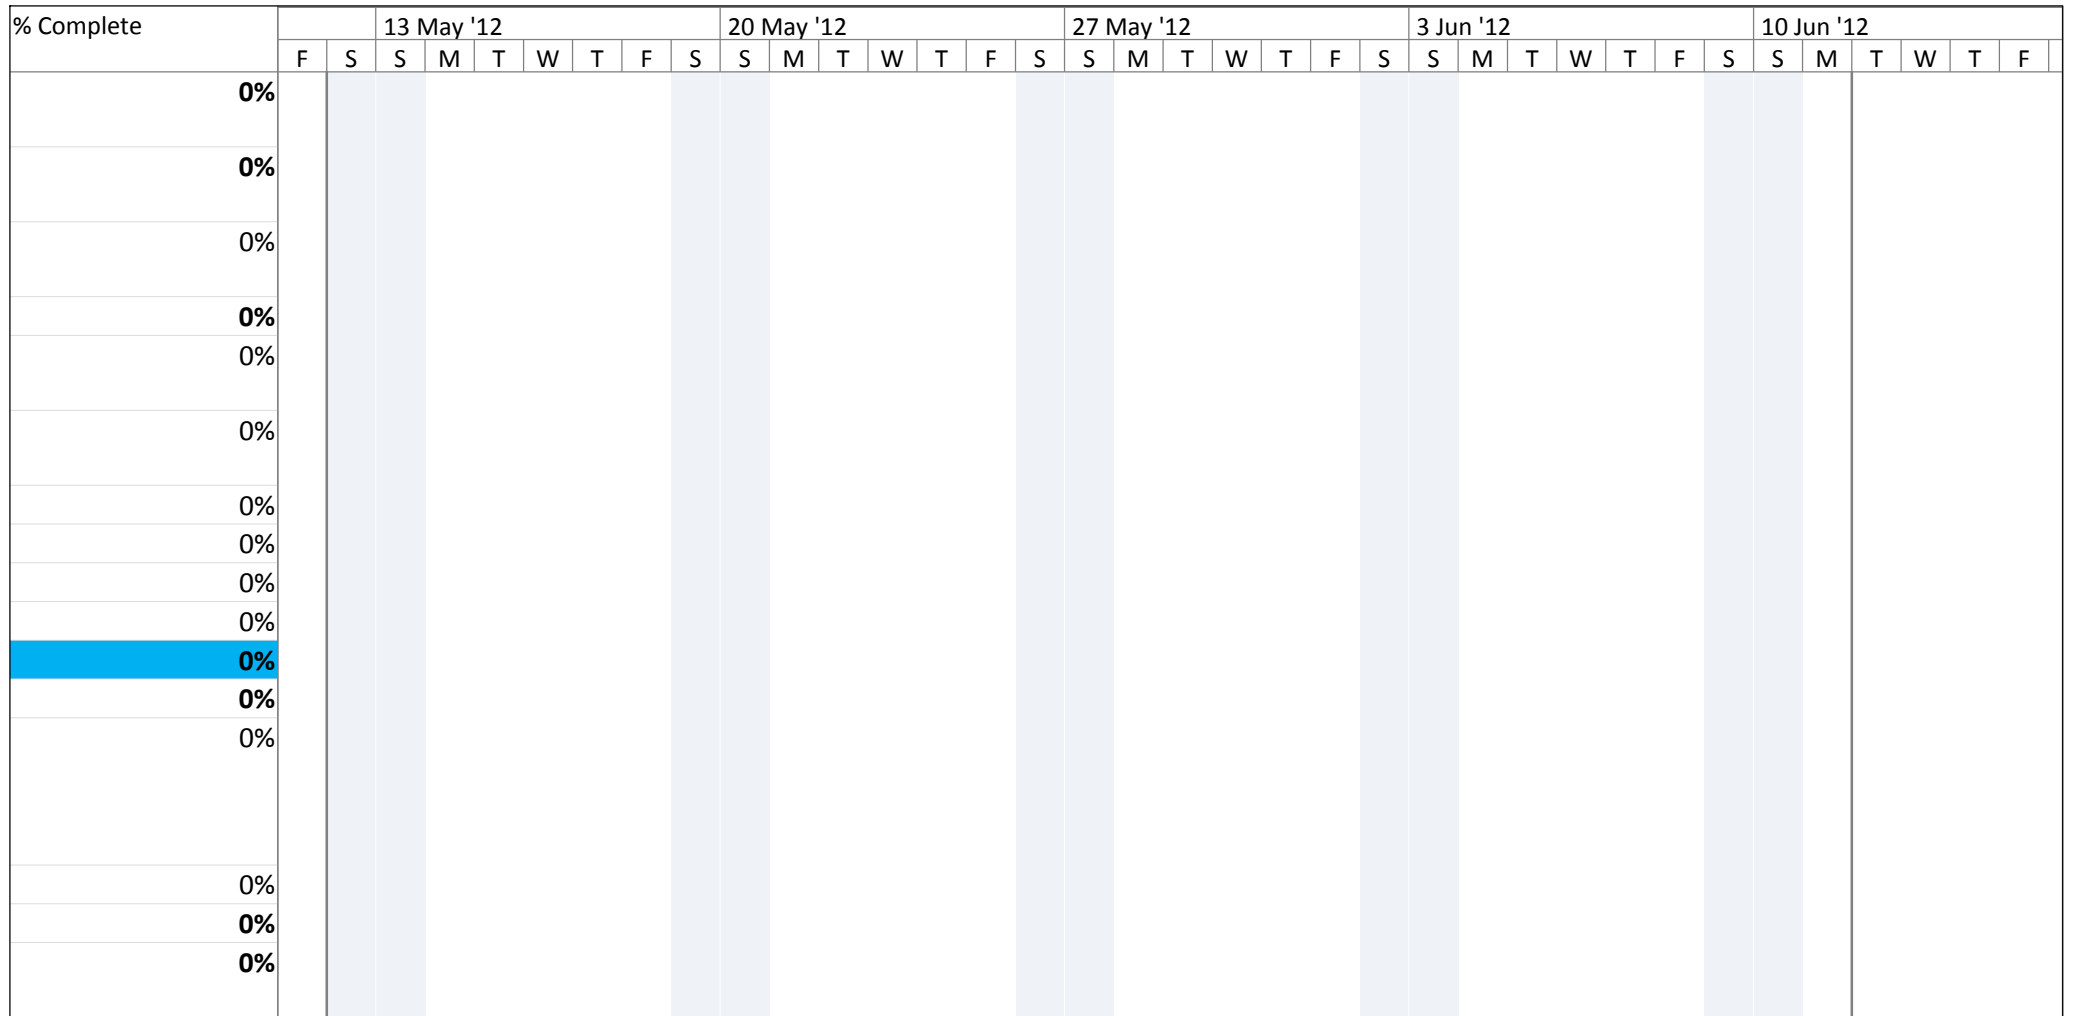

Project: Project Schedule Team Si
 Date: Thu 4/10/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

% Complete	13 May '12							20 May '12							27 May '12							3 Jun '12							10 Jun '12														
	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	
0%																																											
0%																																											
0%																																											
0%																																											
0%																																											
0%																																											
0%																																											



Project: Project Schedule Team Si Date: Thu 4/10/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	
