

Supervisor Meeting

24th Jan 2014

Content

- Progress Update
- Schedule Update
- Task Breakdown
- Demo of Features

Progress Update

- Purpose Driven
- Client has yet to come up with relevant content.
 - Client thinking of strategic time of release.
 - Client requested addition of video bank
 - **Team will come up with relevant content (Free YouTube videos and external API) soon to facilitate mid-term requirement.**
 - **Clarify with client what he wanted , refer to Google image to confirm with his thoughts**
- Mastery-based Coaching
- Client change certain specification:
 - Landing Page UI
 - User need not choose mentor or path the second time
 - Remove all extrinsic motivation content/logic
 - Scores, Time taken , Questions completed
 - Change type of question to be shown
- Client thinking of strategic time of release
- Client thinks team does not completely understand 'extrinsic motivation'
- **Team will come up with relevant content (Self –created audio and GIF images and external APIs) soon to facilitate mid-term requirement.**
- **Team will still continue to meet client weekly and ask client to pen down his exact thoughts**

Progress Update

- Tournament
 - Delayed by 4 days
 - Inserted Wah Chun to mitigate scenario by assisting creation of APIs after completion of Events
 - Create Tournament
 - Client likes design but would now prefer to follow SingPath old UI format (ender version – 2 years ago, Client showed the old content earlier this week)
 - **Notified client that we will edit accordingly but will require more time to make the changes. Client is okay with this arrangement as he believes team is making decent progress.**
 - Join Tournament
 - Completed
 - Still requires Python API to be able to work on the server
 - **Team will dedicate Wah Chun to work on back-end API**

Progress Update


- Tournament (cont'd)
 - Manage Tournament
 - Ongoing
 - Live Ranking
 - Ongoing
- Events Registration
 - Client states this is top priority
 - Client requires tabulation of data such as number of participants, number of visitors, participants' school, etc. that is viewable to the public.
 - **Wah Chun to complete this function after completion of test plan.**
 - **Web dev prototyping suspended for now (until Iteration 8)**
 - **Client is agreeable with this arrangement**

Progress Update

- Test plan
 - Completed for UAT 1 (to be vetted by Prof Ben)
 - Qualitative and quantitative consideration implemented
- Specific documentation of requirements for client
 - Client glanced and said looks good
 - **Team summarized the content to the client verbally as a requirement to mid term and FYP – Client acknowledged**
 - Client wants a documentation of GUI and API of current SingPath for future FYP teams
 - **Team did not promise anything but will consider – based on the progress of the current scope**

Schedule Update

- Status: **Behind Schedule**
- Current Iteration: 6

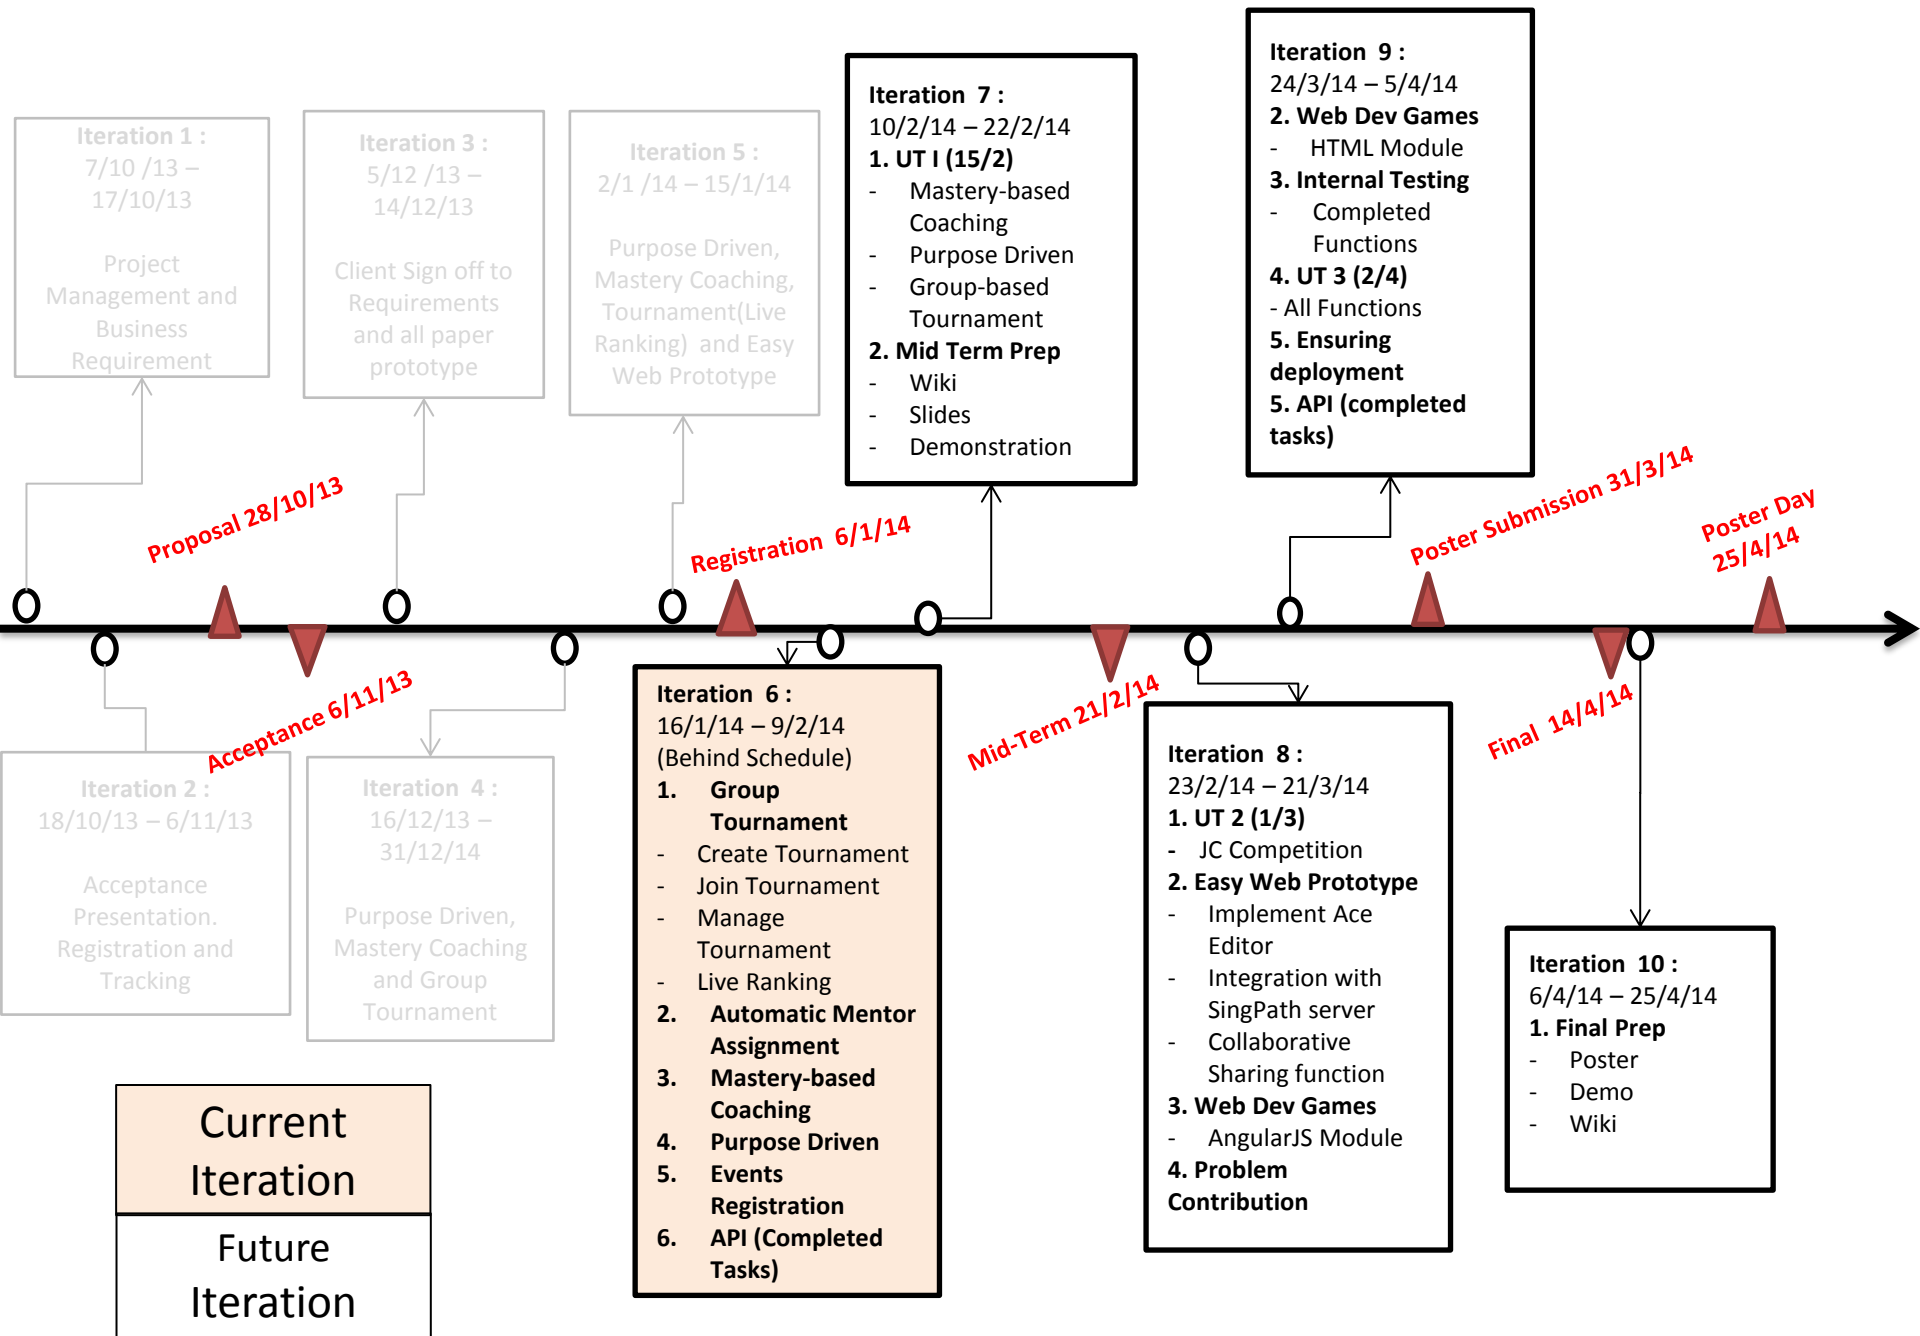

Task Breakdown

Official Role	Name	Allocated Task (Past)	Allocated Task (Upcoming)
Project Manager	Yusof	MB Coaching & Purpose Driven Wiki	Deployment. Relevant APIs
Business Analyst	Shanaaz	Requirement Gathering doc Wiki. (Assist on PM role)	(Assist on PM role until affected functions are completed)
Quality Assurance	Wah Chun	Test Plan	Events/APIs
Lead UI/UX Developer	Fariq	Live Ranking	Live Ranking
Co-Application Developer	Glen	Create and Join Tournament	Manage Tournament
Co-Application Developer	Eng Sen	Manage Tournament	Mentor Assignment
