






















































ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
1			Note: 1 Day (Equivalent to 3 hours)				
2			<b>Inception Phase</b>	<b>39 days</b>	<b>Sat 12/5/12</b>	<b>Wed 20/6/12</b>	<b>All</b>
3			<b>Idea Generation Phase</b>	<b>28 days</b>	<b>Sat 12/5/12</b>	<b>Sat 9/6/12</b>	
4			Idea Discussion Meetings	3 days			All
5			<b>Preliminary Idea Findings</b>	<b>14 days</b>	<b>Sat 12/5/12</b>	<b>Sat 26/5/12</b>	
6			Get popularity Index feature and Internal Consulting Service	7 days	Sat 12/5/12	Sat 19/5/12	Larry
7			Worthy Cause Project- Match-Client	21 days	Sat 12/5/12	Sat 2/6/12	Jeffrey, Kevin
8			Reward System	21 days	Sat 12/5/12	Sat 2/6/12	Kevin
9			Share Worthy Cause project stories	21 days	Sat 12/5/12	Sat 2/6/12	Yi Zao
10			Feedback to Masami (Sponsor Meeting)	0 days	Sat 2/6/12	Sat 2/6/12	Zhang Yingyue
11			<b>Change and Reviewed Idea Findings- Android Application</b>	<b>7 days</b>	<b>Sun 3/6/12</b>	<b>Sun 10/6/12</b>	<b>All</b>
12			Discuss and confirm idea finding during sponsor meetings	0 days	Wed 6/6/12	Wed 6/6/12	All
13			Molecule Concept	5 days	Sun 3/6/12	Fri 8/6/12	Larry, Zheng Keli (T
14			Media Management Concept	5 days	Sun 3/6/12	Fri 8/6/12	Jeffrey, Kevin (TBC)
15			Consolidate All Ideas	1 day	Fri 8/6/12	Sat 9/6/12	Zhang Yingyue
16			Final Review by project managers	1 day	Sat 9/6/12	Sun 10/6/12	Jeffrey, Kevin
17			Start meeting with supervisor and Professor Zhu	0 days	Sat 9/6/12	Sat 9/6/12	All
18			<b>Discussion of main plans for wiki page</b>	<b>0 days</b>	<b>Sat 9/6/12</b>	<b>Sat 9/6/12</b>	<b>All</b>
19			Make updates to wiki page	8 days	Sun 10/6/12	Mon 18/6/12	Yi Zao, Zheng Keli
20			Discuss final adjustments of project scope with Masami (Email)	1 day	Mon 11/6/12	Tue 12/6/12	Zhang Yingyue
21			Consolidation of final changes (in technically defined scope)	5 days	Wed 13/6/12	Mon 18/6/12	Zhang Yingyue, Larr
22			<b>Discussion of project plans and risks for the elaboration phase</b>	<b>0 days</b>	<b>Wed 13/6/12</b>	<b>Wed 13/6/12</b>	<b>All</b>
23			Project managers to make final adjustments to schedule, prepare resources, create risks profile for the elaboration phase	4 days	Thu 14/6/12	Mon 18/6/12	Jeffrey, Kevin
24			Prepare project proposal and review wiki page	1 day	Tue 19/6/12	Wed 20/6/12	Kevin, Jeffrey

Project: Project Schedule Team Si Date: Tue 14/8/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
25			Milestone- Project Proposal	0 days	Wed 20/6/12	Wed 20/6/12	All
26			Buffer Days	0 days	Wed 20/6/12	Wed 20/6/12	All
27			<b>Elaboration Phase (Iteration 2)</b>	<b>19 days</b>	<b>Thu 21/6/12</b>	<b>Tue 10/7/12</b>	<b>All</b>
28			Confirm Idea internally within the team	3 days	Thu 21/6/12	Sun 24/6/12	All
29			Identify the correct Mobile Environment to build upon	3 days	Wed 27/6/12	Sat 30/6/12	Jeffrey
30			Create Use Case Diagrams and Use Case Descriptions	3 days	Sat 30/6/12	Tue 3/7/12	Zhang Yingyue
31			Setup Of Environment	1 day	Tue 3/7/12	Wed 4/7/12	All
32			<b>Learning on the Android Development</b>	<b>8 days</b>	<b>Thu 5/7/12</b>	<b>Fri 13/7/12</b>	<b>All</b>
33			Functional Development	13 days	Thu 5/7/12	Wed 18/7/12	Jeffrey, Kevin, Zhang
34			UI Development	13 days	Thu 5/7/12	Wed 18/7/12	Yi Zao, Zheng Keli
35			Exchange of ideas between functional & UI team happen on 2 occasions on developing application				All
36			Internal team review on learning development, Masami's feedbacks	0 days	Thu 12/7/12	Thu 12/7/12	All
37			<b>Schedule For Functional Development Team</b>				
38			<b>Development Documentation</b>	<b>16 days</b>	<b>Wed 18/7/12</b>	<b>Fri 3/8/12</b>	<b>Kevin, Zhang Yingyue</b>
39			SQL Database data table	3 days	Wed 18/7/12	Sat 21/7/12	Kevin
40			Review of SQL Database data table	13 days	Sat 21/7/12	Fri 3/8/12	Kevin, Zhang Yingyue
41			1st Review by Masami on discussed proposal	0 days	Sun 8/7/12	Sun 8/7/12	All
42			<b>Schedule For UI Development Team</b>				
43			Free Form Diary UI & Newsletter UI	1 day	Sun 8/7/12	Mon 9/7/12	Zheng Keli
44			Administer UI (For Worthy Cause Admin to edit photo into various forms & B1G1 Admin to post good pictures on the B1G1 portal)	3 days	Wed 11/7/12	Sat 14/7/12	Zheng Keli
45			Reward System UI	9 days	Sat 14/7/12	Mon 23/7/12	Zheng Keli
46			Final Check by project manager on overall UI diagram	1 day	Sun 22/7/12	Mon 23/7/12	Kevin
47			UI Mockup 1st Review with Masami	0 days	Mon 23/7/12	Mon 23/7/12	Yi Zao, Zheng Keli




















Project: Project Schedule Team Si Date: Tue 14/8/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
48			Review Of UI Mockup from 1st Review	8 days	Mon 23/7/12	Tue 31/7/12	Zheng Keli
49			UI Mockup 2nd Review with Masami	0 days	Tue 31/7/12	Tue 31/7/12	Yi Zao,Zheng Keli
50			Review of UI Mockup from 2nd Review	3 days	Tue 31/7/12	Fri 3/8/12	Zheng Keli
51			UI Mockup Final Review with Masami	0 days	Fri 3/8/12	Fri 3/8/12	Yi Zao,Zheng Keli
52			<b>Preparation + Rehearsal for Presentation</b>	<b>4 days</b>	<b>Wed 8/8/12</b>	<b>Sun 12/8/12</b>	<b>Jeffrey,Kevin,Zhan</b>
53			Prepare Powerpoint Slides	2 days	Wed 8/8/12	Fri 10/8/12	Yi Zao,Zhang Yingy
54			Updates to wiki page	1 day	Fri 10/8/12	Sat 11/8/12	Yi Zao
55			Final updates to project schedule, risk assessments, learning outcomes, development documents	2 days	Wed 8/8/12	Fri 10/8/12	Kevin
56			Check powerpoint slides and wiki page ready	1 day	Sat 11/8/12	Sun 12/8/12	Kevin
57				0 days	Sun 12/8/12	Sun 12/8/12	Jeffrey,Kevin,Zhang
58			Buffer Days	1 day	Sun 12/8/12	Mon 13/8/12	
59			Acceptance Presentation	0 days	Tue 14/8/12	Tue 14/8/12	Jeffrey,Kevin,Zhang
60			<b>Construction phase (Iteration 3 to 10)</b>	<b>136 days</b>	<b>Tue 17/7/12</b>	<b>Fri 30/11/12</b>	
61			<b>Iteration 3 -Manage Photo Part 1 (Take Photo with App, App Splash Page, Login)</b>	<b>27 days</b>	<b>Tue 17/7/12</b>	<b>Mon 13/8/12</b>	
62			<b>Schedule For Functional Development Team</b>				
63			<b>Development of "Capture Photo" &amp; "Upload Photo" function</b>	<b>27 days</b>	<b>Tue 31/7/12</b>	<b>Mon 27/8/12</b>	<b>Jeffrey,Kevin</b>
64			<b>App Startup Splash Screen</b>	<b>4 days</b>	<b>Wed 18/7/12</b>	<b>Sun 22/7/12</b>	<b>Jeffrey,Kevin</b>
65			Study on how to develop App Startup Splash	1 day	Wed 18/7/12	Thu 19/7/12	Jeffrey,Kevin,Zhang
66			Development of App Startup Screen	2 days	Thu 19/7/12	Sat 21/7/12	Jeffrey,Kevin
67			Debugging for App Startup Screen	1 day	Sat 21/7/12	Sun 22/7/12	Jeffrey,Kevin
68			<b>Login Screen for various users</b>	1 day	Tue 7/8/12	Wed 8/8/12	Kevin
69			[Description] WC team members (Leads to main menu), B1G1 businesses (Leads to web portal)				



















Project: Project Schedule Team Si Date: Tue 14/8/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
70			Study on the development of the login screen	0.5 days	Tue 7/8/12	Tue 7/8/12	Kevin
71			Creation of SQL database till Access Photo Feature Part 1	1 day	Tue 7/8/12	Wed 8/8/12	Kevin
72			Development of Login Screen for various user + Linkage to SQL Database	2 days	Tue 24/7/12	Thu 26/7/12	Kevin
73			Debugging for Login Screen	1 day	Thu 26/7/12	Fri 27/7/12	Kevin,Zhang Yingyu
74			<b>Access Photo Feature</b>	5 days	Fri 3/8/12	Wed 8/8/12	Jeffrey
75			[Description]Entry Fields (Photo, Photo title, Photo description, GPS Location) & Actions: Snap, cancel & retake, delete, upload	1 day	Fri 3/8/12	Sat 4/8/12	
76			Study the development of "Access Photo Features"	1 day	Fri 3/8/12	Sat 4/8/12	
77			<b>Development of Access Photo Features</b>	<b>5 days</b>	<b>Fri 3/8/12</b>	<b>Wed 8/8/12</b>	<b>Jeffrey</b>
78			Actions: Snap, cancel, delete, upload	2 days	Fri 3/8/12	Sun 5/8/12	Jeffrey
79			Photo, Photo Title, Live Feed Update	1 day	Sun 5/8/12	Mon 6/8/12	Jeffrey
80			Debugging for Access Photo Feature	2 days	Mon 6/8/12	Wed 8/8/12	Jeffrey,Zhang Yingyu
81			<b>Schedule For UI Development Team</b>				
82			UI Development for App Startup Splash and Login Screen	8 days	Tue 17/7/12	Wed 25/7/12	Zheng Keli
83			UI Development for Access Photo Feature	5 days	Fri 3/8/12	Wed 8/8/12	Yi Zao,Zheng Keli
84			Debugging for the overall functional application built so far	2 days	Wed 8/8/12	Fri 10/8/12	Jeffrey,Zheng Keli
85			<b>Iteration 4 - Manage Photo Part 2 (Display Photo on diary entry &amp; live feed, Image Cropping)</b>	<b>6 days</b>	<b>Sun 19/8/12</b>	<b>Sat 25/8/12</b>	
86			<b>Development Of Photo Cropping function</b>	<b>6 days</b>	<b>Sun 19/8/12</b>	<b>Sat 25/8/12</b>	
87			Study how to develop the photo cropping function for the photo just added to the application	1 day	Sun 19/8/12	Mon 20/8/12	All
88			Prepare Test cases for Photo Cropping function	1 day	Mon 20/8/12	Tue 21/8/12	Zhang Yingyue
89			<b>Schedule for Functional Development Team</b>				

Project: Project Schedule Team Si Date: Tue 14/8/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	






















ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
90			<b>Crop the original photo taken into any size or dimensions the users see fit</b>	1 day	Wed 22/8/12	Thu 23/8/12	Jeffrey, Kevin
91			After the rectangle is displayed, the unselected area should be cropped	1 day	Wed 22/8/12	Thu 23/8/12	Jeffrey, Kevin
92			<b>Schedule for UI Development Team</b>				
93			Page setup of displaying the picture on a new page in the Android application	1 day	Mon 20/8/12	Tue 21/8/12	Zheng Keli, Yi Zao
94			Create the rectangle to indicate the area of effect of the picture that the user wants preserved after cropping	1 day	Tue 21/8/12	Wed 22/8/12	Yi Zao, Zheng Keli
95			Debugging for the Photo Cropping Function	2 days	Thu 23/8/12	Sat 25/8/12	Jeffrey, Zheng Keli, z
96			<b>Iteration 5 Part 1 - Manage Diary Entry Part 1(View Live Feed &amp; GPS)</b>	<b>22 days</b>	<b>Sat 25/8/12</b>	<b>Sun 16/9/12</b>	
97			<b>Development of live feed function</b>	<b>7 days</b>	<b>Sat 25/8/12</b>	<b>Sat 1/9/12</b>	
98			Learn how to populate the live feeds on the "Special Moments" page and enable the worthy cause admin from the Drupal site to see into these live feeds + further requirements gathering (how the list is going to populate)	2 days	Sun 26/8/12	Tue 28/8/12	All
99			Prepare test cases for "Live Feed" function	1 day	Tue 28/8/12	Wed 29/8/12	Zhang Yingyue
100			<b>Schedule for Functional Development Team</b>				
101			<b>Populate the live updates accordingly for the "Special Moments" page in the app and "Captured Momenets" page in drupal</b>	<b>4 days</b>	<b>Mon 27/8/12</b>	<b>Fri 31/8/12</b>	
102			As more live feeds are added, populate the lists in the appropriate order and length in the page as decided by the sponsor	1 day	Mon 27/8/12	Tue 28/8/12	Kevin
103			Populate the live updates on the B1G1 drupal site & create basic templates for the other miscellaneous categories	2 days	Mon 27/8/12	Wed 29/8/12	Jeffrey

Project: Project Schedule Team Si  
Date: Tue 14/8/12



















Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names
104		<b>Schedule for UI development team</b>				
105		Embolden words, decorate and format accurately the "Special Moments" page	1 day	Tue 28/8/12	Wed 29/8/12	Yi Zao,Zheng Keli
106		Convert the populated lists generated into a slideshow format & decorate the templates	2 days	Wed 29/8/12	Fri 31/8/12	Yi Zao,Zheng Keli
107		Debugging for View Live Feed Function	2 days	Fri 31/8/12	Sun 2/9/12	Jeffrey,Zheng Keli,
108		<b>Development of GPS feature</b>	<b>14 days</b>	<b>Sun 2/9/12</b>	<b>Sun 16/9/12</b>	
109		Learn how to retrieve coordinates from the Android phone using an application and then query the coordinates using an existing database service to get the location name	3 days	Sun 2/9/12	Wed 5/9/12	All
110		Prepare test cases for the GPS feature	1 day	Wed 5/9/12	Thu 6/9/12	Zhang Yingyue
111		<b>Schedule for Functional Development Team</b>				
112		Display the latitude and longitude coordinates from the GPS feature on the Diary Entry Page	1.5 days	Wed 5/9/12	Thu 6/9/12	Jeffrey,Kevin
113		Display the location name using the Google API and coordinates given by the GPS on the diary entry page	2.5 days	Fri 7/9/12	Sun 9/9/12	Jeffrey,Kevin
114		<b>Schedule for UI Development Team</b>				
115		(Optional Requirement- to discuss with Masami) Develop the google map on B1G1 app indicating the precise locaton given by the GPS	3 days	Sun 9/9/12	Wed 12/9/12	Yi Zao,Zheng Keli
116		Debugging for GPS feature	3 days	Wed 12/9/12	Sat 15/9/12	
117		Buffer Days	2 days	Sat 15/9/12	Mon 17/9/12	
118		<b>Milestone 3 - UAT 1</b>	<b>13 days</b>	<b>Sun 16/9/12</b>	<b>Sat 29/9/12</b>	<b>All</b>
119		<b>Milestone 4 - Mid Term Presentation</b>	<b>0 days</b>	<b>Mon 1/10/12</b>	<b>Mon 1/10/12</b>	<b>All</b>
120		<b>Iteration 5 Part 2 - Manage Diary Entry Part 2 (Live Feed Sharing on Twitter &amp; Facebook)</b>	<b>6 days</b>	<b>Sat 6/10/12</b>	<b>Fri 12/10/12</b>	

Project: Project Schedule Team Si Date: Tue 14/8/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
121			Learn about facebook & twitter API to post the live feed from the app to facebook or twitter + final requirements gathering on this function	1.5 days	Sat 6/10/12	Sun 7/10/12	All
122			Prepare test cases for "Live Feed Sharing" function	1 day	Sun 7/10/12	Mon 8/10/12	Zhang Yingyue
123			<b>Schedule for Functional Development Team</b>				
124			Display the live feed on facebook- Integration with mobile app and facebook	1.5 days	Mon 8/10/12	Tue 9/10/12	Jeffrey
125			Display the live feed on twitter - Integrating mobile app with twitter	1.5 days	Mon 8/10/12	Tue 9/10/12	Kevin
126			<b>Schedule for UI Development Team</b>				
127			Prepare the pop-up options for the user to select where to upload their live feeds	1.5 days	Mon 8/10/12	Tue 9/10/12	Yi Zao,Zheng Keli
128			Integrate the developments done by the UI & Functional development team	0.5 days	Tue 9/10/12	Tue 9/10/12	Jeffrey,Kevin,Yi Zao,Zheng Keli
129			Debug for live feed sharing on twitter & facebook	1.5 days	Wed 10/10/12	Thu 11/10/12	Jeffrey,Kevin,Zhang
130			Buffer Days	1 day	Thu 11/10/12	Fri 12/10/12	
131			<b>Iteration 6 - Manage Diary Entry Comments</b>	<b>14 days</b>	<b>Fri 12/10/12</b>	<b>Fri 26/10/12</b>	
132			<b>Development of Comment on Diary Entry function</b>	<b>7 days</b>	<b>Fri 12/10/12</b>	<b>Fri 19/10/12</b>	
133			Learn to develop "Comment On Diary Entry" function in the mobile application and the drupal framework + final requirements gathering on this function	1.5 days	Fri 12/10/12	Sat 13/10/12	All
134			Prepare test cases for "Comment On Diary Entry" function	1 day	Sat 13/10/12	Sun 14/10/12	Zhang Yingyue
135			<b>Schedule for Functional Development Team</b>				
136			Connect to the database for the live feed and comments any live feeds in the application	1 day	Sun 14/10/12	Mon 15/10/12	Jeffrey,Kevin
137			Create the calculation logic required for the "Captured Moments" page based on the comments posted by a worthy cause organisation	2 days	Mon 15/10/12	Wed 17/10/12	Jeffrey,Kevin

Project: Project Schedule Team Si  
Date: Tue 14/8/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names
138		<b>Schedule for UI Development Team</b>				
139		Conduct UI development for "Discuss This!" Page	1 day	Sun 14/10/12	Mon 15/10/12	
140		Create the graphical chart and the statistical figures as illustrated by the "Captured Moments" page	2 days	Mon 15/10/12	Wed 17/10/12	
141		Integration of "Discuss This!" Page and the backend connection to enable comments to be posted	0.5 days	Mon 15/10/12	Mon 15/10/12	Jeffrey, Kevin, Yi Zao, Zheng Keli
142		Integration of the calculation logic with the statistical figures	1 day	Wed 17/10/12	Thu 18/10/12	Jeffrey, Kevin, Yi Zao
143		Integration of the calculation logic with the graph diagram	1 day	Thu 18/10/12	Fri 19/10/12	Jeffrey, Kevin, Yi Zao
144		<b>Development of View/Moderate Comments By Admin On Drupal</b>	<b>7 days</b>	<b>Fri 19/10/12</b>	<b>Fri 26/10/12</b>	
145		Learn to develop on drupal to allow view/moderate comments by admin + final requirements gathering on this function	1.5 days	Fri 19/10/12	Sat 20/10/12	All
146		Prepare test cases for "View/Moderate Comments by Admin" function	1 day	Sat 20/10/12	Sun 21/10/12	Zhang Yingyue
147		<b>Schedule for Functional Development Team</b>				
148		Method to retrieve the complete diary entry and comments from database	2 days	Fri 19/10/12	Sun 21/10/12	
149		<b>Schedule for UI Development Team</b>				
150		Create a template similar to "Discuss This" page but have a function that allows the admin to delete posts	2 days	Fri 19/10/12	Sun 21/10/12	
151		Integration of the delete function to the backend comments	1 day	Sun 21/10/12	Mon 22/10/12	
152		Debugging "View/Moderate Comments by Admin" function	2 days	Mon 22/10/12	Wed 24/10/12	
153		Buffer Days	2.5 days	Wed 24/10/12	Fri 26/10/12	
154		<b>Iteration 7 - Manage WC Team Members</b>	<b>10 days</b>	<b>Fri 26/10/12</b>	<b>Mon 5/11/12</b>	
155		<b>Development of "Create &amp; Access worthy cause team member accounts" function</b>	<b>10 days</b>	<b>Fri 26/10/12</b>	<b>Mon 5/11/12</b>	

Project: Project Schedule Team Si  
Date: Tue 14/8/12








Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	





















ID	Task Mode	Task Name	Duration	Start	Finish	Resource Names
156		Learn to create user accounts and populate the user accounts under B1G1 Giving's Team Members	1.5 days	Fri 26/10/12	Sat 27/10/12	All
157		Prepare test cases for "Manage team members" function	1 day	Sun 28/10/12	Mon 29/10/12	Zhang Yingyue
158		<b>Schedule For Functional Development Team</b>				
159		Accept values from the create account fields and store it in the database	1 day	Mon 29/10/12	Tue 30/10/12	Kevin
160		Logic to retrieve the user accounts from the database and populate it on the "Manage Team Member's Page"	2 days	Mon 29/10/12	Wed 31/10/12	Jeffrey
161		<b>Schedule for UI Development Team</b>				
162		Develop the user interface for the "Create Accounts field"	0.5 days	Mon 29/10/12	Mon 29/10/12	Yi Zao,Zheng Keli
163		Develop the user interface for the "B1G1 Giving's Team Members" Section	0.5 days	Tue 30/10/12	Tue 30/10/12	Yi Zao,Zheng Keli
164		Develop the user interface for the rest of the "Manage team members" page	1 day	Tue 30/10/12	Wed 31/10/12	Yi Zao,Zheng Keli
165		Debug for live feed sharing on twitter & facebook	2 days	Wed 31/10/12	Fri 2/11/12	Jeffrey, Kevin, Yi Zao
166		Buffer Days	3 days	Fri 2/11/12	Mon 5/11/12	
167		<b>Milestone 5 - UAT 2</b>	<b>14 days</b>	<b>Mon 5/11/12</b>	<b>Mon 19/11/12</b>	<b>All</b>
168		<b>Transition Phase (Iteration 8)</b>	<b>18 days</b>	<b>Mon 19/11/12</b>	<b>Fri 7/12/12</b>	<b>All</b>
169		<b>UI touchup and final debugging</b>	<b>7 days</b>	<b>Mon 19/11/12</b>	<b>Mon 26/11/12</b>	
170		Final Integration Of Codes	3 days	Thu 22/11/12	Sun 25/11/12	Jeffrey, Kevin, Yi Zao
171		Debug entire application & testing	3 days	Mon 19/11/12	Thu 22/11/12	Jeffrey, Kevin, Zhang
172		Make UI more consistent with the requirements of sponsor	3 days	Mon 19/11/12	Thu 22/11/12	Yi Zao, Zheng Keli
173		Buffer Days	1 day	Sun 25/11/12	Mon 26/11/12	
174		<b>Project Presentations</b>	<b>1 day</b>	<b>Tue 17/7/12</b>	<b>Wed 18/7/12</b>	
175		Preparation of project management documents	3 days	Thu 29/11/12	Sun 2/12/12	Jeffrey, Kevin


Project: Project Schedule Team Si  
Date: Tue 14/8/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

ID		Task Mode	Task Name	Duration	Start	Finish	Resource Names
176			Prepare presentation slides	3 days	Thu 29/11/12	Sun 2/12/12	Yi Zao,Zheng Keli
177			Prepare speech presentation	1 day	Sun 2/12/12	Mon 3/12/12	All
178			Buffer Days	1 day	Mon 3/12/12	Tue 4/12/12	
179			Milestone 6 - Final Presentation	6 days	Thu 29/11/12	Wed 5/12/12	
180			Prepare Poster for Poster Day	2 days	Wed 5/12/12	Fri 7/12/12	All
181			Milestone 7 - Poster Day	0 days	Fri 7/12/12	Fri 7/12/12	


Project: Project Schedule Team Si  
Date: Tue 14/8/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

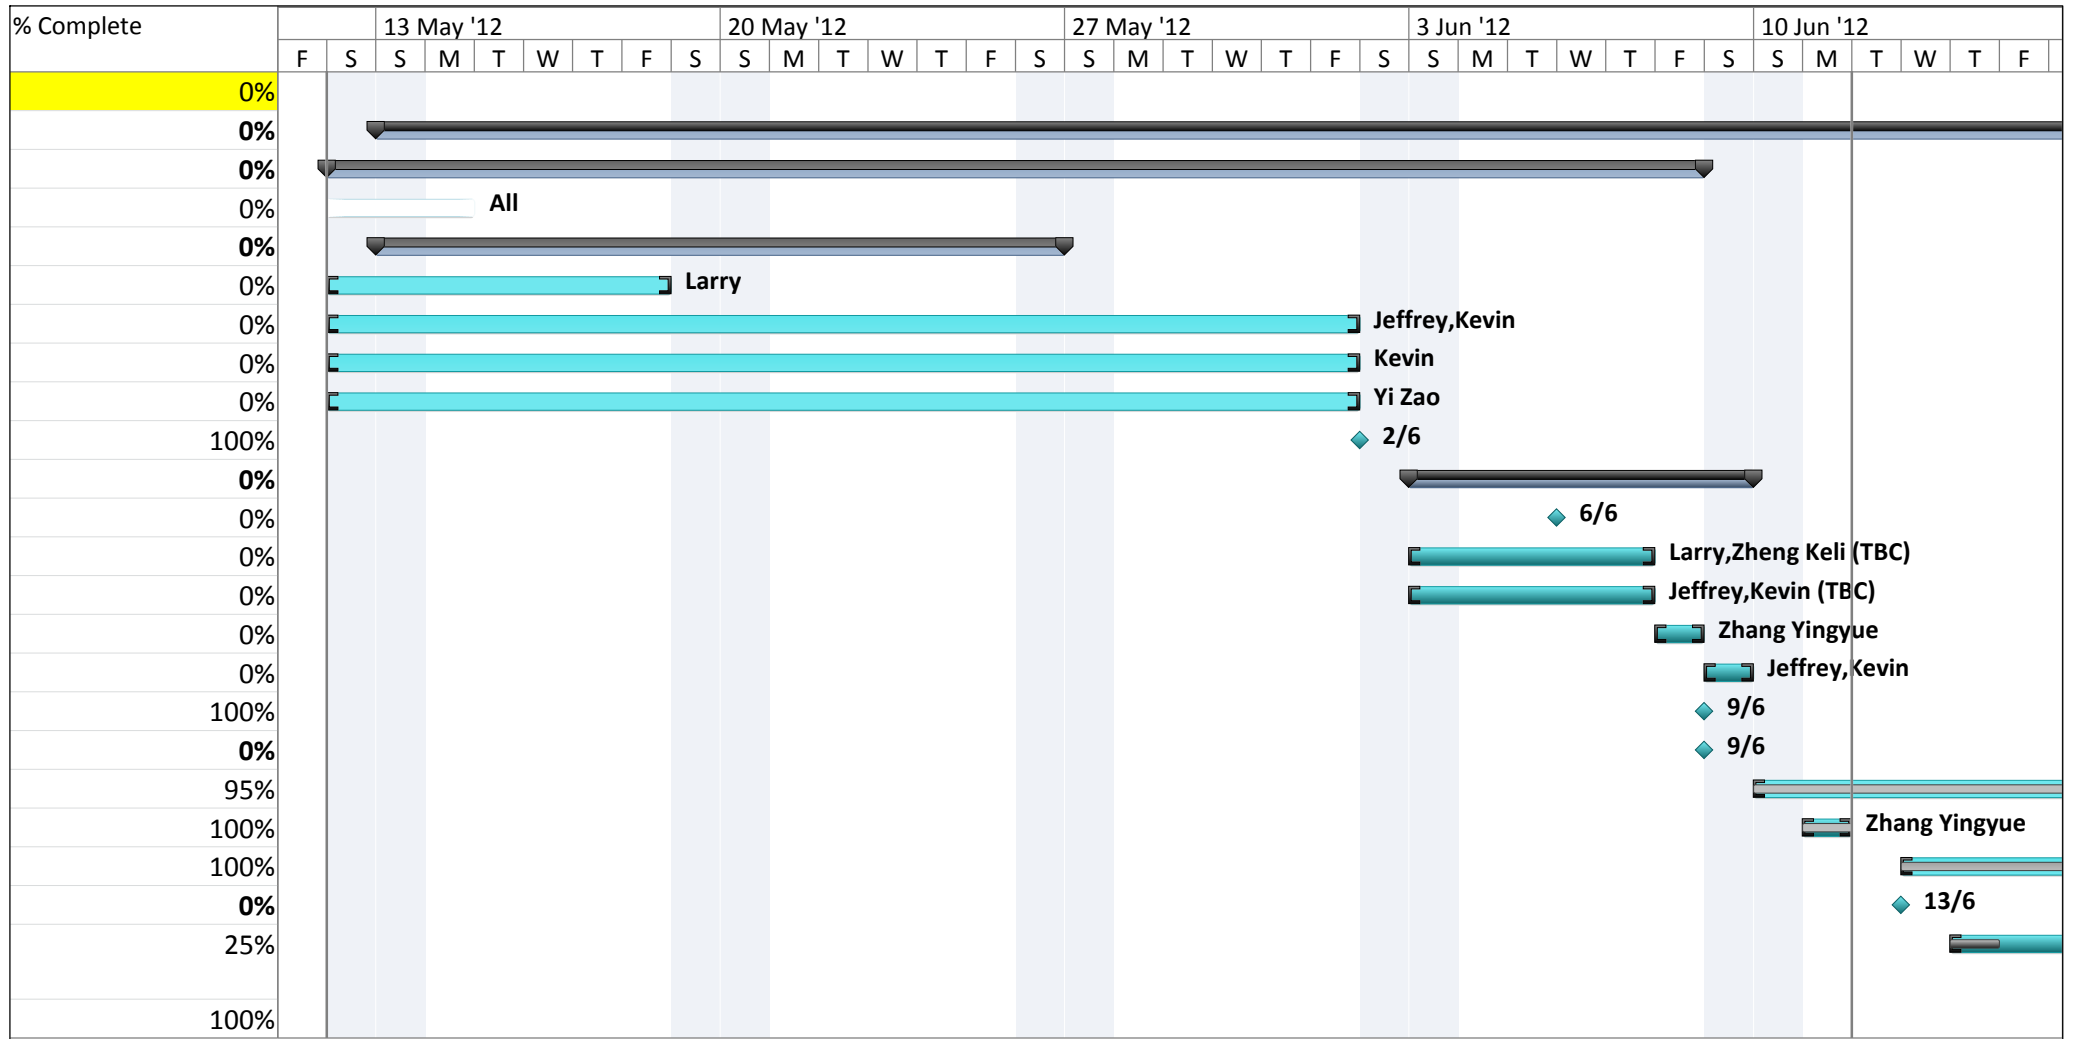

Project: Project Schedule Team Si  
Date: Tue 14/8/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

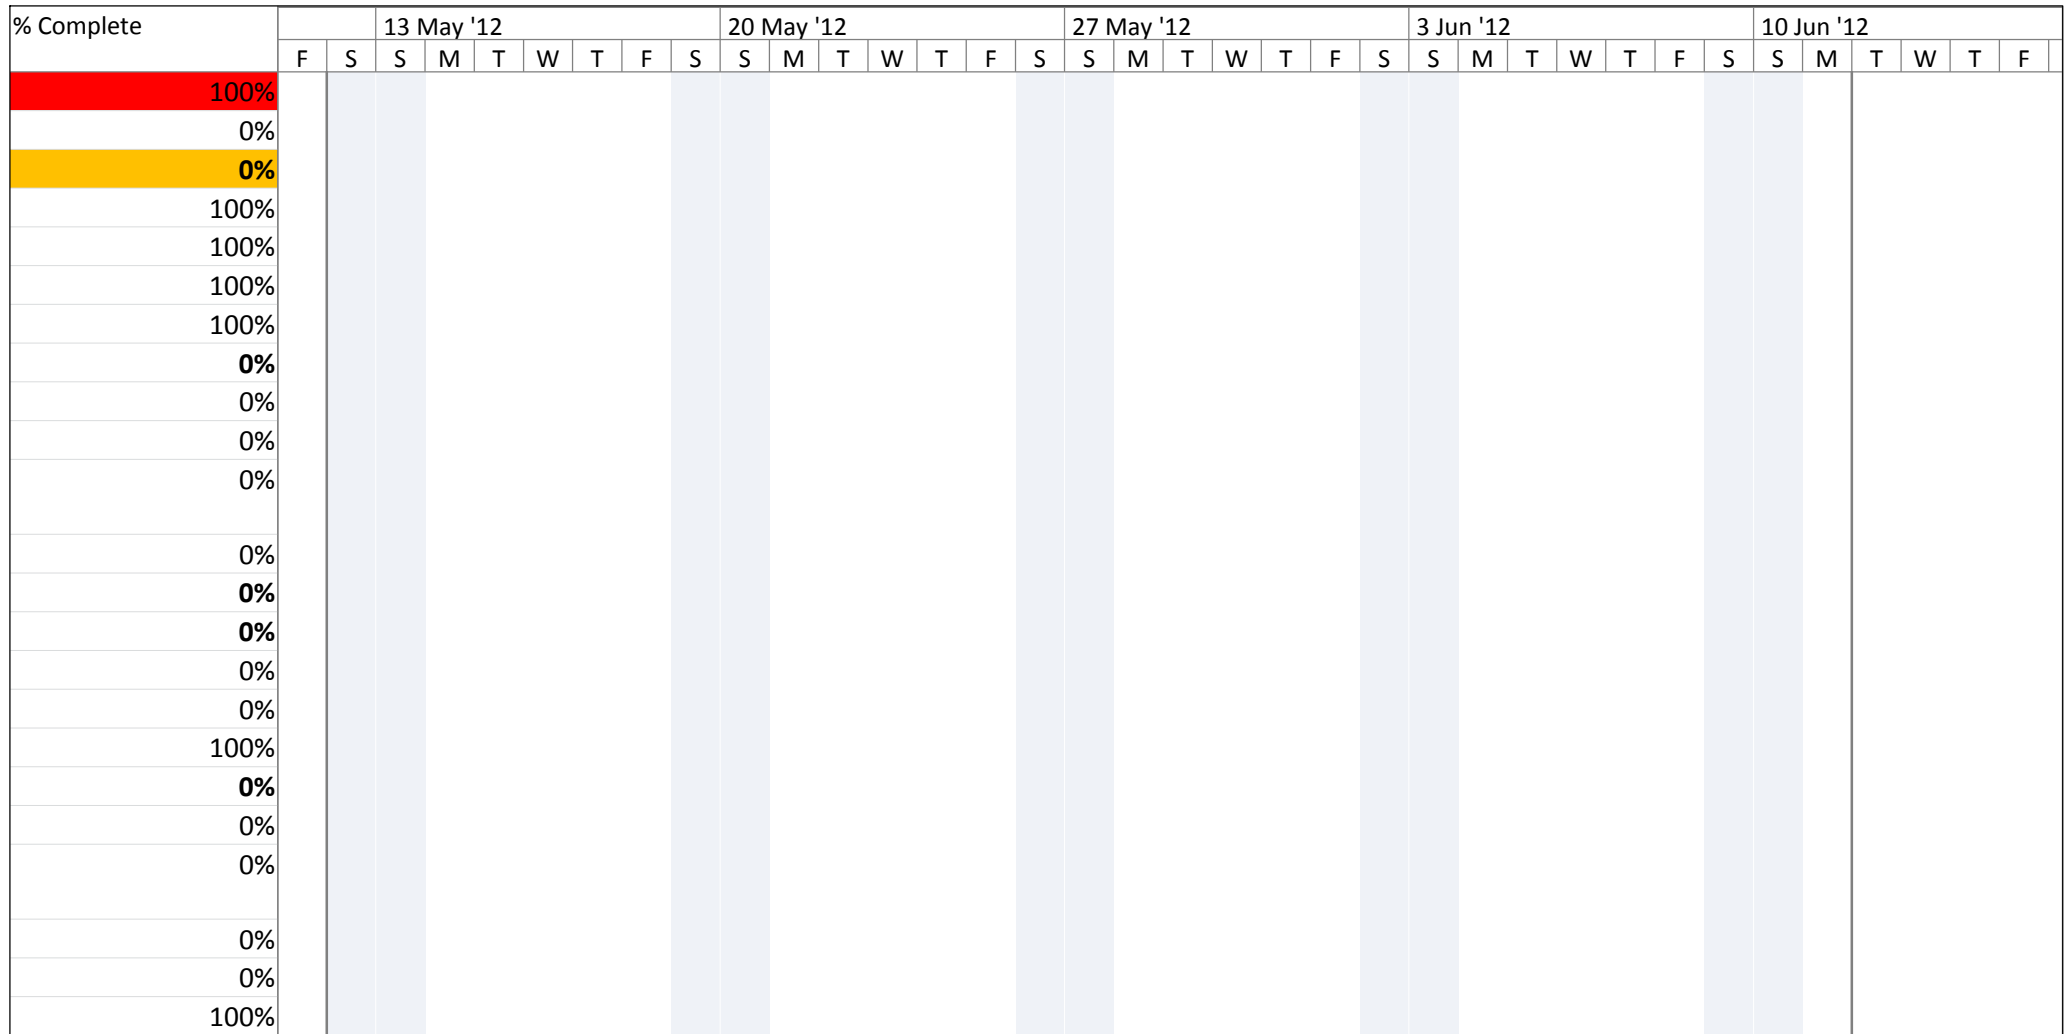

Project: Project Schedule Team Si  
Date: Tue 14/8/12

Task		External Milestone		Manual Summary Rollup	
Split		Inactive Task		Manual Summary	
Milestone		Inactive Milestone		Start-only	
Summary		Inactive Summary		Finish-only	
Project Summary		Manual Task		Deadline	
External Tasks		Duration-only		Progress	

















% Complete	13 May '12							20 May '12							27 May '12							3 Jun '12							10 Jun '12														
	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	F	S	S	M	T	W	T	
0%																																											
0%																																											
0%																																											
0%																																											
0%																																											
0%																																											



Project: Project Schedule Team Si Date: Tue 14/8/12	Task		External Milestone		Manual Summary Rollup	
	Split		Inactive Task		Manual Summary	
	Milestone		Inactive Milestone		Start-only	
	Summary		Inactive Summary		Finish-only	
	Project Summary		Manual Task		Deadline	
	External Tasks		Duration-only		Progress	
